

Project No. 1251-100

Crude Oil Tank Farms Project, Agrood Area 30 (Module-1)



System ID

030-LP-008

System
Description

Tank-4 Fire Protection System

Sr.	Pre-Commissioning and Commissioning Dossier Index	Applicable (Yes/No)
1	Mechanical Completion Certificate (MCC)	
2	Ready for Startup Certificate (RFSU)	
3	System Punch Lists	
4	System Limits Marked Up P&ID	
5	System Index	
6	Piping Pre-Commissioning	
	6.01) Piping Test Packs	
	6.02) Piping Pre-commissioning Check Lists	
7	Piping Commissioning	
	7.01) Service Test, GLT, CLT and N2 Purging Certificates	
	7.02) Piping Commissioning Check Lists	
Sr.	Pre-Commissioning and Commissioning Dossier Index	Applicable (Yes/No)
8	Mechanical Pre-Commissioning	
	8.01) System Mechanical Index	
	8.02) Equipment Drawings	
	8.03) Equipment Datasheets	
	8.04) Boxing-up Certificates	

	8.05) Grouting Certificates	
	8.06) Pre-Alignment Certificates	
	8.07) Mechanical Pre-Commissioning Checklists	
9	Mechanical Commissioning	
	9.01) Final Alignment Certificates	
	9.02) Motor Solo Run Certificates	
	9.03) Mechanical Run Test (MRT) Certificates	
	9.04) Mechanical Commissioning Checklists	
	9.05) Mechanical Supplier Check Lists & Reports	
10	Instrumentation Pre-Commissioning	
	10.01) System Instrument Index	
	10.02) Instrument Data Sheets	
	10.03) Instrument Cable Schedule	
	10.04) System Instrumentation Wiring Diagram	
	10.05) Hook-up Drawing (Mechanical & Pneumatic)	
	10.06) Instruments Cables Schedule	
	10.07) Instruments Cables Laying Certificates	
	10.08) Instruments Cables Termination Certificates	
	10.09) Instruments Cables Testing Certificates	
	10.10) Instruments Calibration Certificates	
	10.11) Instrument Loop Checks Certificates	
	10.12) Instrumentation Pre-Commissioning Check Lists	
	10.13) Instrumentation Supplier Check Lists & Reports	
11	Instrumentation Commissioning	
	11.01) Instrumentation Function Test Certificates	
	11.02) Instrumentation Supplier Check Lists & Reports	
Sr.	Pre-Commissioning and Commissioning Dossier Index	Applicable (Yes/No)
12	Electrical Pre-Commissioning	
	12.01) System Electrical Index	
	12.02) Electrical Drawings	
	12.03) Motor Datasheets	
	12.04) Electrical Cables Schedule	
	12.05) Electrical Cables Laying Certificates	
	12.06) Electrical Cables Testing Certificates	
	12.07) Electrical Cables Termination Certificates	
	12.08) FAT Reports & Certificates	
	12.09) SAT Reports & Certificates	
	12.10) Electrical Pre-Commissioning Check Lists	
	12.11) Electrical Supplier Check Lists & Reports	

13	Electrical Commissioning	
	13.01) Electrical -Commissioning Check Lists	
	13.02) Electrical Supplier Check Lists & Reports	
14	Red Marked-up Drawings	
	14.01) P&ID	
	14.02) Instrumentation Drawings	
	14.03) Electrical Drawings	



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



COMPLETION DOSSIER

030-LP-008

Tank-4 Fire Protection System



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

1-Mechanical Completion Certificate (MCC)

SYSTEM MECHANICAL COMPLETION CERTIFICATE (MCC)

PROJECT TITLE : CRUDE OIL TANK FARM(AGROOD AREA

PROJECT No : 1251-100

SYSTEM NAME : Tank-4 Fire Protection System




SYSTEM ID : 030-LP-008

THIS IS TO CERTIFY THAT:

- THE ABOVE SYSTEM HAS BEEN FABRICATED, ERECTED, INSTALLED AND TESTED TO THE REQUIREMENTS OF THE CONTRACT DRAWINGS, SPECIFICATIONS, THE APPLICABLE CODES AND STANDARDS.
- ALL PRE-COMMISSIONING RELEVANT ACTIVITIES, TESTS, INSPECTIONS AND CHECKS HAVE BEEN CARRIED OUT FOR THIS SYSTEM AND FOUND ACCEPTABLE.
- Q/C DOCUMENTATION OF THE ABOVE SYSTEM HAS BEEN AUDITED BY THE CUSTOMER SITE QUALITY CONTROL AND FOUND COMPLETED.
- ALL PUNCH LIST ITEMS CATEGORY (A) IN THIS SUBSYSTEM WERE CLEARED.
- THIS SYTEM IS MECHANICALLY COMPLETED ON THE DATE 22/06/2021 AND READY FOR COMMISSIONING (RFC) WITH THE FOLLOWING EXCEPTIONS.

EXCEPTIONS :

NOTE: ACCEPTANCE OF THE ABOVE SYSTEM DOES NOT RELIEVE ENPPI/CONSTRUCTION CONTRACTOR FROM THEIR CONTRACTUAL OBLIGATIONS AND RESPONSIBILITIES.

COMPANY	PETROJET	ENPPI	PPC
NAME	M. abd allah	Mohamed Abbass	
TITLE	Q.C engineer		M. omer
SIGNATURE			
DATE	22/6/2021		



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

2- Ready for Startup Certificate (RFSU)

READY FOR START UP CERTIFICATE

PROJECT TITLE : EGPC CRUDE OIL TANK FARMS PROJECT (AGROOD-02)

PROJECT No. : 1251-100



SYSTEM /AREA /PLANT : Tank-4 Fire Protection System

SYSTEM /AREA /PLANT No. : 030-LP-008

THIS IS TO CERTIFY THAT:

- THE MENTIONED SYSTEM /AREA /PLANT IS READY FOR START UP WHERE ALL MECHANICAL WORKS, PRECOMMISSIONING AND COMMISSIONING ACTIVITIES HAVE BEEN SUCCESSFULLY COMPLETED.
- MECHANICAL COMPLETION CERTIFICATE(S) FOR THE MENTIONED SYSTEM / AREA / PLANT HAVE BEEN SIGNED.
- ISSUANCE OF THIS READY FOR START UP CERTIFICATE(S) SHALL NOT RELIEVE CONTRACTOR(S) FROM THEIR OBLIGATIONS TO COMPLETE THE REMAINING SYSTEMS NOR FROM THEIR WARRANTY OBLIGATIONS AND OTHER PROVISIONS OF THE CONTRACT.
- THE FOLLOWING EXCEPTIONS AGREED TO BE CLEARED AFTER START UP AND WILL NOT PREVENT START UP ACTIVITIES.

EXCEPTIONS :

COMPANY	CONSORTIUM	PPC
NAME	Ahmed El Shate	M. Saleh
TITLE	Commissioning Manager	Site Manager
SIGNATURE		
DATE	1-7-2021	01/07/2021

System ID	030-LP-008
System Description	Tank-4 Fire Protection System

3- System Punch Lists

PROJECT TITLE : CRUDE OIL TANK FARM PROJECT (AGROOD AREA)

PROJECT NUMBER : 01251-100

DISCIPLINE: Loss Prevention

SYSTEM NAME: Tank 04 Fire Protection System



SYSTEM ID: 030-LP-008

SUB-SYSTEM NAME:

SUB-SYSTEM ID:

[illegible]

CAT: CATEGORY(A,B,C), ACTION BY: (ENPPI,CONST.CONTRACTOR,SUPPLIER.....) , DISP: DISCIPLINE(PIP,MECH,ELECT,INST.....)

COMPANY	PTJ	ENPPI	PMC
NAME		Abdullah Fathy	
SIGN.			
DATE			M. Omar



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

4- System Limits Marked Up P&ID

System ID	030-LP-008
System Description	Tank-4 Fire Protection System

5- System Index



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

6- Piping Pre-Commissioning



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

6.01- Piping Test Packs

System ID	030-LP-008
System Description	Tank-4 Fire Protection System

6.02- Piping Pre-commissioning Check Lists



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

7- Piping Commissioning



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

7.01- Service Test, GLT, CLT and N2 Purging Certificates







Service Test Certificate of Completion and Acceptance

Client	Egyptian General Petroleum Corporation (EGPC)
Project No.	1251-100
Project Description	Crude Oil Tank Farm Project
Location	Agrood Area 30 (Module-01)
System	030-LP-008 (Tank-04 Fire Protection System)
Loop No.	030-LP-008 (Tank-04 Fire Protection System)
Test Medium	Firefighting Water
Test Pressure	Put in service
Completion Date	22-6-2021
Attachments	Leak Test Loop Marked-up P&ID

Remarks

- This is to certify that the system described in this certificate of completion has been Leak Tested using water after final reinstatement and mechanical completion for the system in accordance with the requirements of the scope of work.
- The test has been witnessed by client representatives and accepted as complete in all aspects on the data marked on the certificate of completion and acceptance.
- The test has been completed to the client satisfaction.

Performed by PETROJET	Supervised by ENPPI	Approved by PPC
Name: 	Name: Ahmed El Shorbe	Name: H. Saleh
Title: Hydrotest Engineer	Title: Commissioning Manager	Title: Site Manager
Signature: 	Signature: 	Signature: 
Date: 22/6/2021	Date: 22-6-2021	Date: 01/07/2021

محضر اجتماع

بخصوص تجربة شبكات التبريد والإطفاء لمستودع رقم (٤)

بموقع الشركة العامة بعجروود

إنه في يوم الخميس الموافق ٢٠٢١/٠٧/٠١م، تم إجراء تجارب اختبار شبكات التبريد والإطفاء لمستودع رقم (٤) بموقع الشركة العامة بعجروود، بحضور ممثلي قطاع السلامة بشركة أنابيب البترول.

- وقد تبين أن المنظومة تعمل بكفاءة وبنجاح.

شركة أنابيب البترول

وليد عبدالمعظم

إمام محمد
المستودع

شركة أنبي

أحمد الشافعي
1-7-2021







Service Test Certificate of Completion and Acceptance

Client	Egyptian General Petroleum Corporation (EGPC)
Project No.	1251-100
Project Description	Crude Oil Tank Farm Project
Location	Agrood Area 30 (Module-01)
System	030-LP-008 (Tank-04 Fire Protection System)
Loop No.	030-LP-008 (Tank-04 Fire Protection System)
Test Medium	Firefighting Water
Test Pressure	Put in service
Completion Date	22-6-2021
Attachments	Leak Test Loop Marked-up P&ID

Remarks

- This is to certify that the system described in this certificate of completion has been **Leak Tested using water** after final reinstatement and mechanical completion for the system in accordance with the requirements of the scope of work.
- The test has been witnessed by client representatives and accepted as complete in all aspects on the data marked on the certificate of completion and acceptance.
- The test has been completed to the client satisfaction.

Performed by PETROJET	Supervised by ENPPI	Approved by PPC
Name: 	Name: Ahmed El Shorbe	Name: H. Saleh
Title: Hydrotest Engineer	Title: Commissioning Manager	Title: Site Manager
Signature: 	Signature: 	Signature: 
Date: 22/6/2021	Date: 22-6-2021	Date: 01/07/2021



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID 030-LP-008

System Description Tank-4 Fire Protection System

7.02- Piping Commissioning Check Lists



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

8- Mechanical pre-Commissioning



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

8.01- System Mechanical Index



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

8.02- Equipment Drawings



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

8.03- Equipment Datasheets



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

8.04- Boxing-up Certificates



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

8.05- Grouting Certificates



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

8.06- Pre-Alignment Certificates



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

8.07- Mechanical Pre-Commissioning Checklists



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

9- Mechanical Commissioning



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

9.01- Final Alignment Certificates



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

9.02- Motor Solo Run Certificates



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

9.03- Mechanical Run Test (MRT) Certificates



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

9.04- Mechanical Commissioning Checklists



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

9.05- Mechanical Supplier Check Lists & Reports



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

10- Instrumentation Pre-Commissioning



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

10.01- System Instrument Index



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

10.02- Instrument Data Sheets



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

10.03- Instrument Cable Schedule



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

10.04- System Instrumentation Wiring Diagram



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

10.05- Hook-up Drawing (Mechanical & Pneumatic)



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

10.06- Instruments Cables Schedule



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

10.07- Instruments Cables Laying Certificates



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

10.08- Instruments Cables Termination Certificates



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

10.09- Instruments Cables Testing Certificates



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

10.10- Instruments Calibration Certificates



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

10.11- Instrument Loop Checks Certificates



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

10.12- Instrumentation Pre-Commissioning Check Lists



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

10.13- Instrumentation Supplier Check Lists & Reports



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

11- Instrumentation Commissioning



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

11.01) Instrumentation Function Test Certificates

MINUTES OF MEETING	PROJECT TITLE : EGPC Crude Oil Tank Farms Project (AGROOD 30) (Module 01)							
	PROJECT No : 1251-100	DATE : 5-9-2021						
	CUSTOMER : EGPC (PPC)							
LOCATION : Agrood, Suez, EGYPT		MEETING DATE : 5-9-2021						
WRITTEN BY : Ahmed El Shafie		DEPARTMENT : Commissioning & Startup						
MEETING No : [MEETING No]		FILE No :						
<u>PURPOSE OF MEETING:</u> <p style="text-align: center;">Fire & Gas Cause & Effect Verification Finalization for Agrood Area 30 (Module-01)</p>								
<u>ATTENDEES:</u> <table style="width: 100%; border: none;"> <tr> <td style="text-align: center; width: 33%;"><u>ENPPI</u></td> <td style="text-align: center; width: 33%;"><u>PETROJET</u></td> <td style="text-align: center; width: 33%;"><u>PPC</u></td> </tr> <tr> <td style="text-align: center;">Ali Ashraf</td> <td style="text-align: center;">Sobhy Selem</td> <td style="text-align: center;">M. Omar</td> </tr> </table>			<u>ENPPI</u>	<u>PETROJET</u>	<u>PPC</u>	Ali Ashraf	Sobhy Selem	M. Omar
<u>ENPPI</u>	<u>PETROJET</u>	<u>PPC</u>						
Ali Ashraf	Sobhy Selem	M. Omar						
<u>DISTRIBUTION:</u> 								

MINUTES OF MEETING (Cont'd)			
PROJECT No : 1251-100		MEETING No : [MEETING No]	MEETING DATE : 5-9-2021
ITEM No	DESCRIPTION OF DISCUSSION	ACTION BY	DATE
	<ul style="list-style-type: none"> • This close-out meeting was held between ENPPI, PETROJET and PPC to certify the completion of Fire and gas cause-and-effect verification for Agrood area 30 entirely. • Fire and gas cause-and-effect verification have been tested, witnessed, and approved by PPC. • Signing off this MOM does not relieve any contractor from their contractual obligations. <p>Exceptions:</p> <p>* GD-013 shall be fixed (cleared) Sobhy</p> <p>* 2 smoke detectors in battery rooms.</p> <p>* 4 Gas detectors ZAM modules.</p>		
	<p>Enppi petrojet PPC</p> <p>Ali Ashraf Sobhydeen M. Omar</p>		



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

11.02- Instrumentation Supplier Check Lists & Reports



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

12- Electrical Pre-Commissioning



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

12.01- System Electrical Index

030-LP-008 Tank-4 Fire Protection System
030-LP-008 Tank-4 Fire Protection System
030-LP-008 Tank-4 Fire Protection System
030-LP-008 Tank-4 Fire Protection System
030-LP-008 Tank-4 Fire Protection System
030-LP-008 Tank-4 Fire Protection System
030-LP-008 Tank-4 Fire Protection System
030-LP-008 Tank-4 Fire Protection System

Loss Prevention
Loss Prevention
Loss Prevention
Loss Prevention
Loss Prevention
Loss Prevention
Loss Prevention
Loss Prevention

030-PSH-008
030-GD-004
030-LHD-007
030-LHD-008
030-FD-004
030-PSH-007A
030-PSH-007B
030-PSH-007C
030-PSH-007D

Pressure Switch High
Combustible Gas Detector
Electrical Linear Heat Detector
Electrical Linear Heat Detector
Flame Detector (Triple Infrared)
Pressure Switch High
Pressure Switch High
Pressure Switch High
Pressure Switch High

Checklist
Checklist
Checklist
Checklist
Checklist
Checklist
Checklist
Checklist

LP-10 A
LP-13 A
LP-13 A
LP-13 A
LP-13 A
LP-10 A
LP-10 A
LP-10 A




Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)




System ID	030-LP-008
System Description	Tank-4 Fire Protection System


12.02- Electrical Drawings



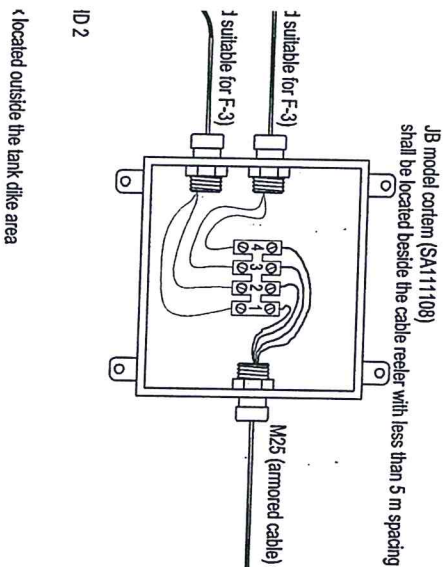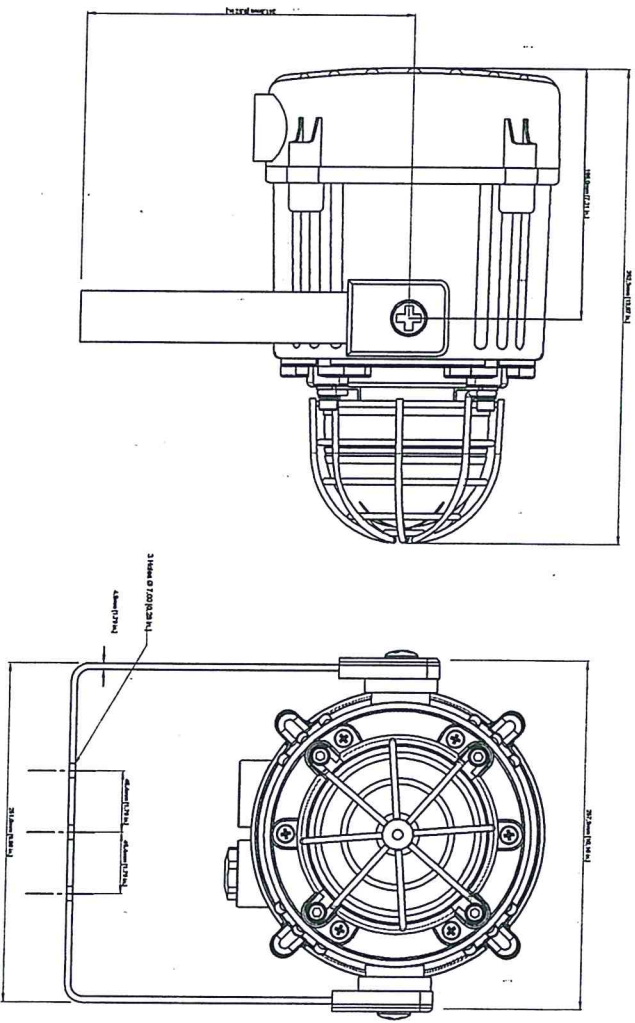
- Qty. 2 M12 glands BM-XS
- Qty. 1 adaptor M12Female x M20 male
- Qty. 1 adaptor M12Female x M25 male





Electrical DC wiring

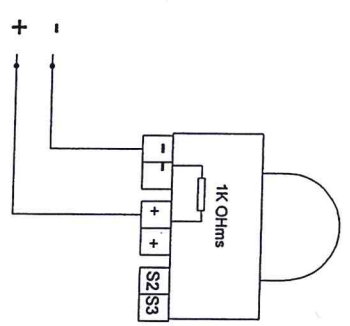

REV	DATE	DESCRIPTION
1	2018	ISSUED FOR APPROVAL


ABB TURBOCHARGERS S.A.
 د.ع. ا.ب.ب. ت.ر.ب.و.ك.ا.ر.ج.ي.ر.س. س.أ.
Enppi
 ENPPI PROJECT NUMBER 4
 5355 West Alsborno St Suite 200
 Tel: + (1) 832-698-4548 Fax: +
 Email: sales@enppi.com

Project Name: EGPC CRUDE OI


DRAWING TITLE
 INSTRUMENT TERMINATI
 HOOK UP DETAIL

SCALE
 NONE

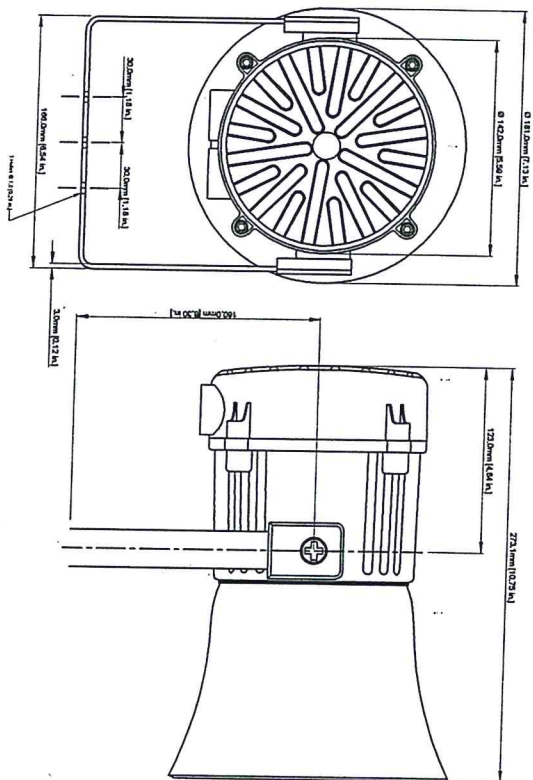DRAWING NUMBER
 SBS-JOB503-DC18-118-011



ELECTRICAL DC WIRING

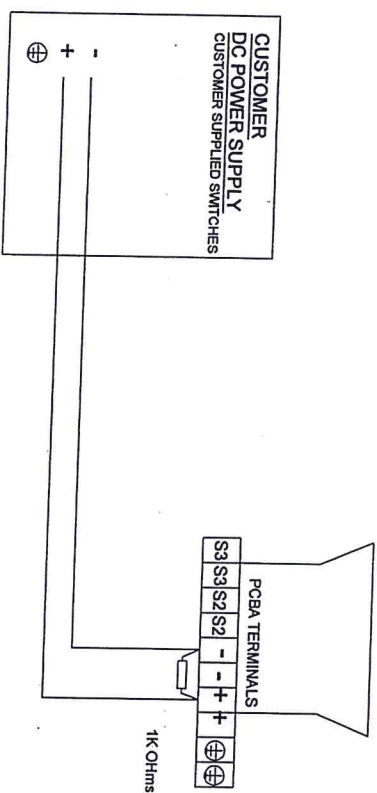

REV	DATE	DESCRIPTION
1	1/1/20	ISSUED FOR APPROVAL
2		
3		
4		
5		

ABR TURBOCHARGERS S.

مركبات توربوشارجERS S.

Enppi

ENGINEERS FOR THE PETROLEUM AND ENPI PROJECT NUMBER

555 West Alabama St Suite 200
Tulsa, Oklahoma 74103
Tel: +1 (918) 532-6986-9424 Fax
Email: sales@abrt.com

SBS

555 West Alabama St Suite 200
Tulsa, Oklahoma 74103
Tel: +1 (918) 532-6986-9424 Fax
Email: sales@abrt.com

SCALE: NONE

Project Name: EGPC CRU

INSTRUMENT TERMINA

HOOK UP DETA

DRAWING NUMBER: SBS-J08503-DC18-118-01

Honey

Searchpoint Optima Plus SPECIFICATIONS



Searchpoint Optima Plus Specification		
Use	Searchpoint Optima Plus is an advanced, Point-Infrared, flammable gas detector certified for use in potentially explosive atmospheres	
Measuring Range	0-100% LEL, wide selection of Hydrocarbon gas and vapor calibrations. Different measuring ranges and solvent calibrations available for specialist applications	
Signal Output	4-20mA autosensing sink or source	
Inhibit	1-3mA (Default 2mA)	
Warning	0-6mA (Default 3mA *)	
Fault	0mA (IART® units adjustable to 1mA)	
Over Range	20-21.5mA (Default 21mA)	
Digital Output	Optional Multidrop Modbus RS485 (via DX100(M)), Optional HART® over 4-20mA output (HART® version 7)	
Material	316 stainless steel	
Weight	1.6kg	
Accuracy	Optima Plus (Hydrocarbon) Baseline < ±1% FSD, 50% FSD < ±2% FSD Optima Plus (Ethylene) Baseline < ±2% FSD, 50% FSD < ±3% FSD	
Repeatability	< ±2% FSD at 50% FSD	
Linearity	< 5% FSD	
Response Time	T50 < 3 seconds, T90 < 4 seconds (methane)	
Operational and Certified	-40°C to +65°C temperature range	
Long Term Stability (as defined in EN 60079-29-1)	Baseline	Methane 100 %LEL Range: ≤ ± 2 %FSD Ethylene 100 %LEL Range: ≤ ± 4 %FSD
	50 %FSD	Methane 100 %LEL Range: ≤ ± 4 %FSD Ethylene 100 %LEL Range: ≤ ± 5 %FSD
Drift Over Temperature Range (-40 °C to 65 °C)	Baseline	≤ ± 2 %FSD
	50 %FSD	Methane 100 %LEL Range: ≤ ± 0.131 %FSD per °C Ethylene 100 %LEL Range: ≤ ± 0.078 %FSD per °C
Variation with Pressure	0.1% (of reading) per mbar	
Power Supply	18-32Vdc (24Vdc nom), < 4.5W max	
Environmental Protection	IP 66 / 67	
Diagnostics (and Re-calibration)	Via certified Hand-held Interrogator, or optional IART® communications	
Safety Approvals	UL / CSA: Class 1, Div 1, groups B, C, and D (-40°C to +65°C) IECEx: Ex d IIC Ib IIIc T86°C (T _{amb} -40°C to +55°C) or T96°C (T _{amb} -40°C to +65°C) IP66/67 ATEX: BAS99ATEX2259X II 2 GD Ex d IIC Gb Ex Ib IIIc Db T96°C (T _{amb} -40°C to +65°C) T86°C (T _{amb} -40°C to +55°C) IP 66/67	
Performance Approvals	CSA C22.2 152., FM ANSI/ISA-12.13.01., EN 60079-29-1 (BVS 03 ATEX G 016 X)	
Functional Safety	IEC61508 Safety Integrity Level 2	
EMC Compliance	EN 50270:2006	
Software	EN 50271:2010	

* Note for ATEX compliance the warning value should not be set between 3 and 5mA

Find out more

www.honeywellanalytics.com

Toll-free: 800.538.0363

Please Note:

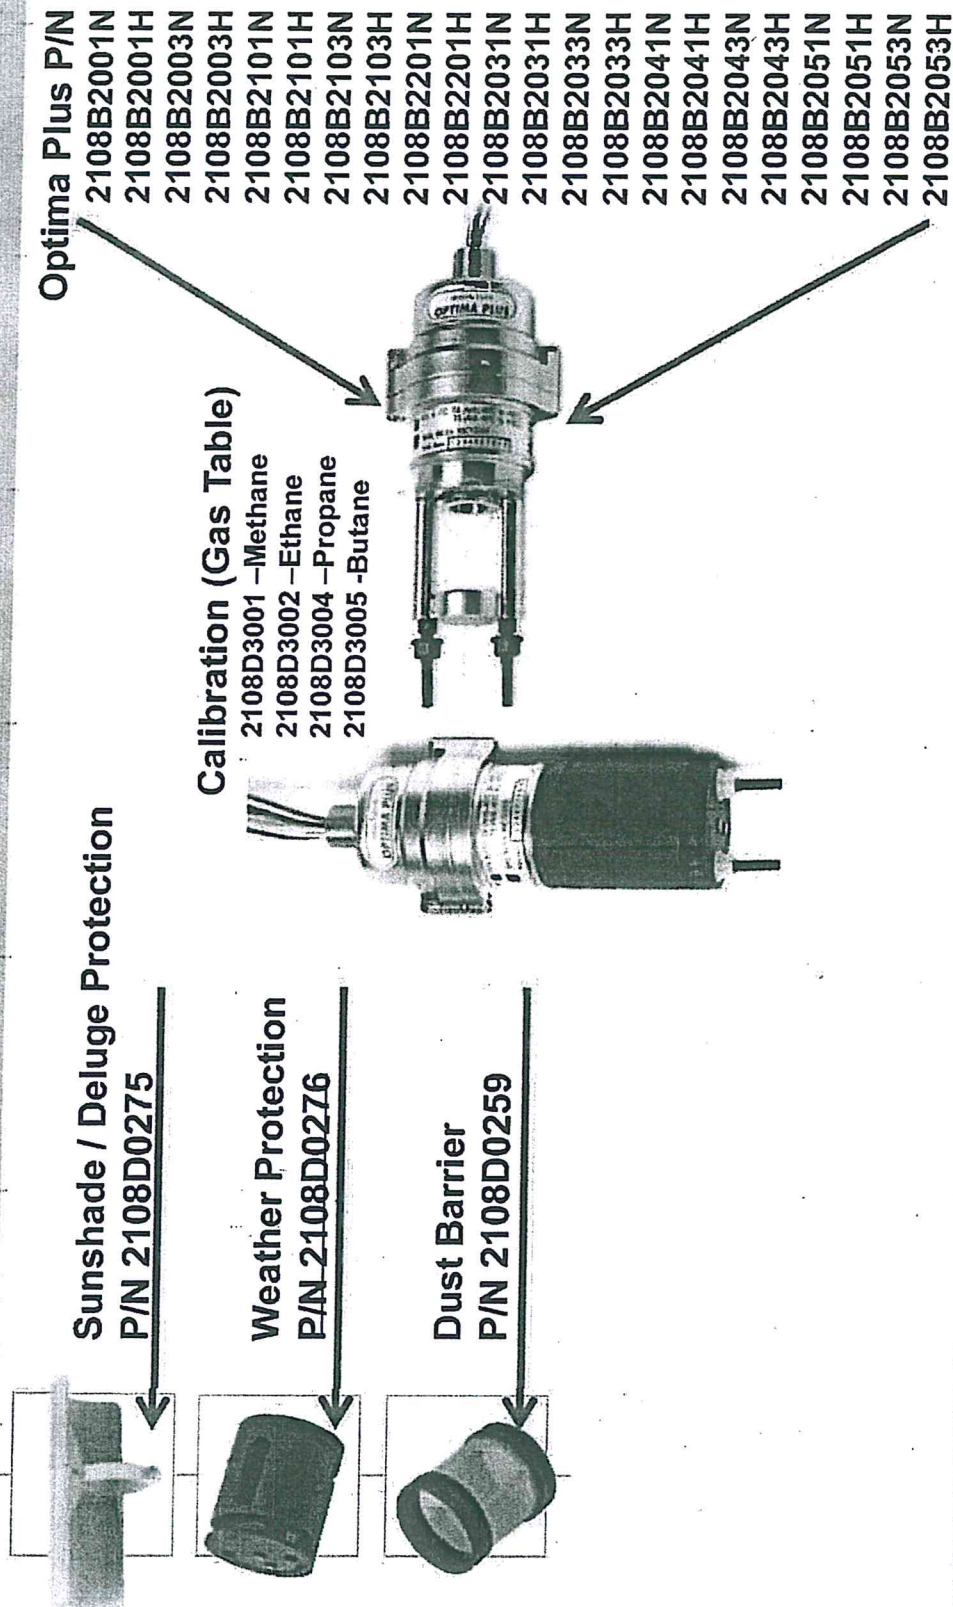
While every effort has been made to ensure accuracy in this publication, no responsibility can be accepted for errors or omissions. Data may change, as well as legislation, and you are strongly advised to obtain copies of the most recently issued regulations, standards, and guidelines. This publication is not intended to form the basis of a contract.

SS0276_v2 4/13
© 2013 Honeywell Analytics

Honeywell

→ Honeywell.com

Optima Plus Part No Decodification 2108N4000N/H



Searchpoint Optima Plus



Why Infrared?

- Failsafe operation
- Fast speed of response
- Reduced routine maintenance
- Immune to catalytic poisons
- Long operating life
- Works in inert atmospheres

Why Searchpoint Optima Plus is the right choice...

- Experience gained from over 100,000 units installed worldwide
- Improved reliability
- Optional HART® over 4-20mA output
- Can detect a wide range of hydrocarbon gases including solvents
- Increased reliability with no moving parts
- Increased stability from self compensating optics
- Immune to long term component drift
- Remote functional gas test facility
- Certified for North American and European Hazardous areas
- Increased false alarm rejection
- Increased uptime with contaminated optics warning
- Dynamic Heating Control ensures condensation free optics
- No undetected failures
- Improved diagnostics
- Integral event logging
- Reduced power consumption
- Certified to many hazardous area classification schemes including: European (ATEX), UL, CSA, IECEx and more

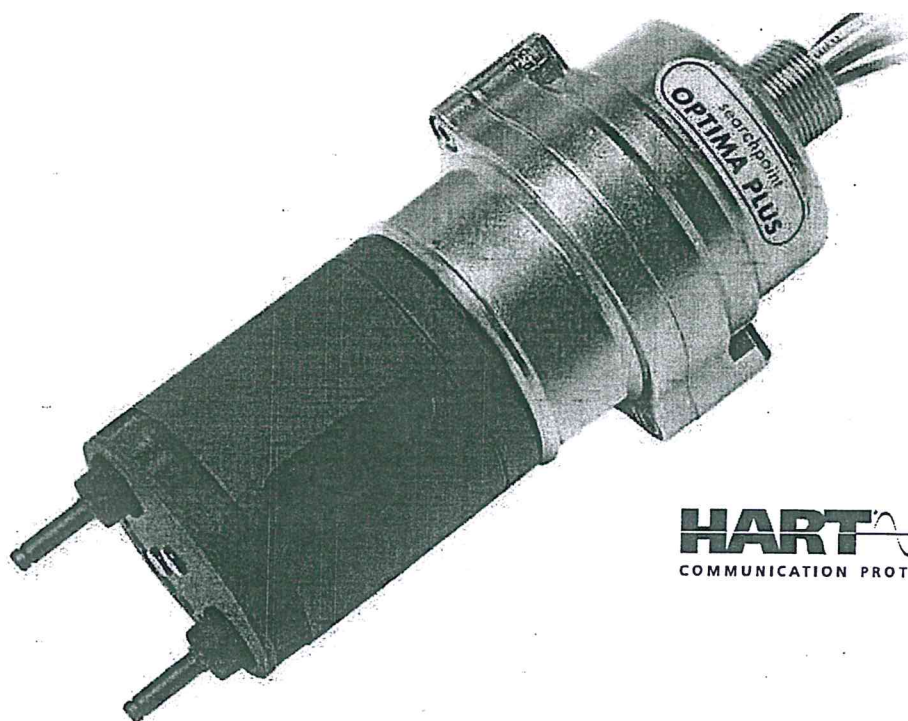
Market leading point infrared Hydrocarbon gas detector offering proven performance and sensitivity

With over 40 years experience in the design, manufacture, installation and maintenance of point infrared gas detection, Honeywell Analytics currently has a Worldwide installed base of over 100,000 infrared point Hydrocarbon gas detectors in a wide spectrum of applications from light industrial to the most demanding of offshore petrochemical environments.

Searchpoint Optima Plus is an infrared point Hydrocarbon gas detector certified for use in potentially explosive atmospheres. The unit's infrared detection principle offers the fastest speed of response and fail-to-safe operation, ensuring that your plant is compliant, your personnel are protected and your production process can deliver maximum uptime. Reduced routine maintenance, when compared with conventional electro-catalytic based gas detectors, provides low ongoing cost of ownership. The development of advanced internal fault diagnostics and false alarm rejection algorithms ensures that Searchpoint Optima Plus delivers the highest level of operational integrity.


Typical applications include environments that may suffer from the presence of catalytic poisons or inhibitors, or where there are harsh environmental conditions forcing increased time between routine maintenance, for example; offshore oil and gas platforms, floating production storage and offloading (FPSO) vessels, tankers, onshore oil and gas terminal refineries, LNG / LPG bottling plants, gas compressor / metering stations, gas turbine power plants, refineries, solvent printing and coating plants.

Over 100 gas and vapour calibrations are available. For a list of detectable gases and vapours, please contact our Customer Support team or your local distributor.



HART 
COMMUNICATION PROTOCOL

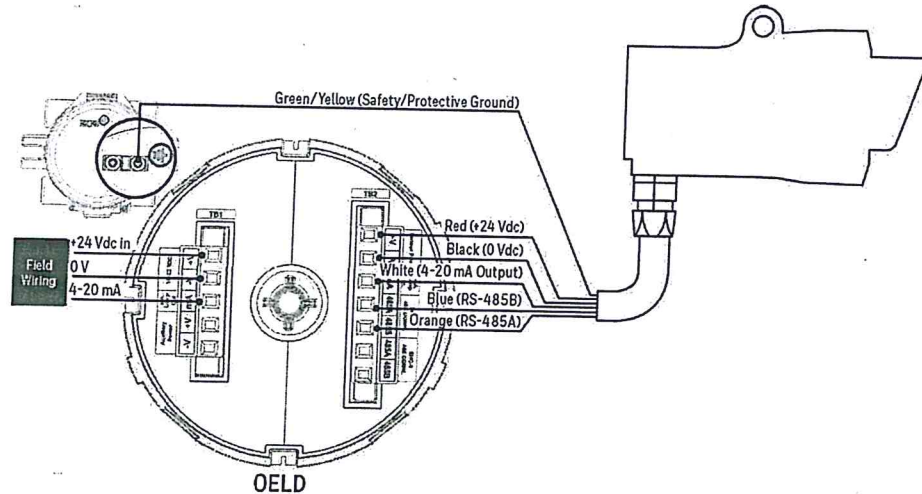
Connecting the OELD to Searchline Excel



<Figure 10. Wiring Diagram for Searchline Excel>

The earth bonding arrangement must ensure that the maximum peak voltage between the unit case earth and any field cable conductor is less than 350V. Voltages in excess of this can cause permanent damage to the units' internal RFI protection filters.

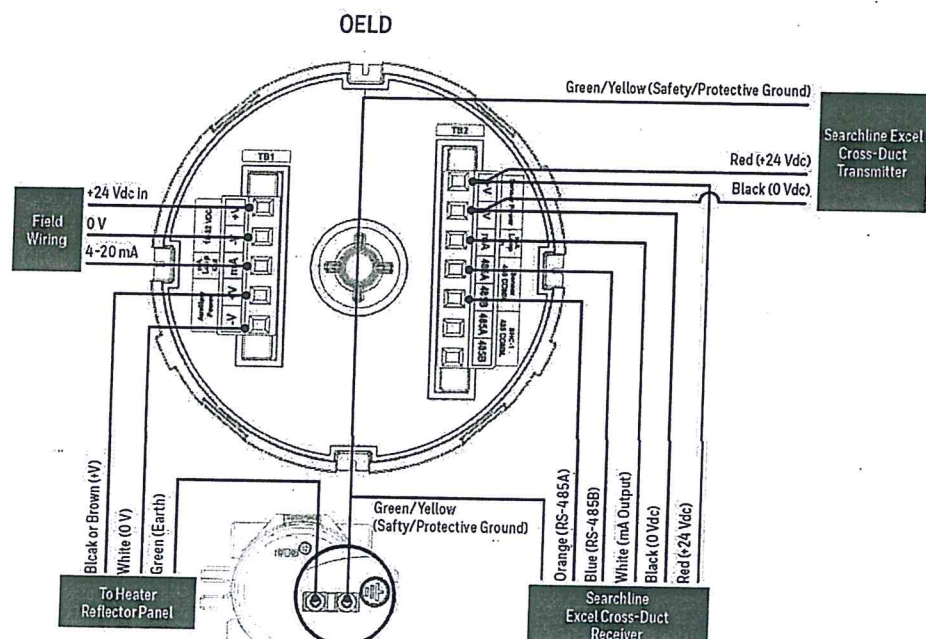
Connecting the OELD to Searchline Excel Cross-Duct (XD)



<Figure 11. Wiring Diagram for Searchline Excel Cross-Duct>

The earth bonding arrangement must ensure that the maximum peak voltage between the unit case earth and any field cable conductor is less than 350V. Voltages in excess of this can cause permanent damage to the units' internal RFI protection filters.

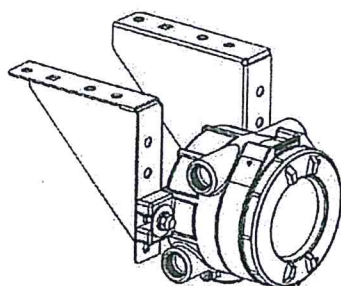2.2.2 Ceiling Mount Bracket Kit (1226A0355)




The Ceiling Mount Bracket Kit (1226A0355) allows the OELD to be mounted to the ceiling. The kit includes two stainless steel ceiling mount brackets, bolts and nuts.

Note

When considering the final mounting position using the Ceiling Mount Bracket Kit, consider the ability to see the OELD display when installed.

<Figure 3. Ceiling-Mounted OELD>

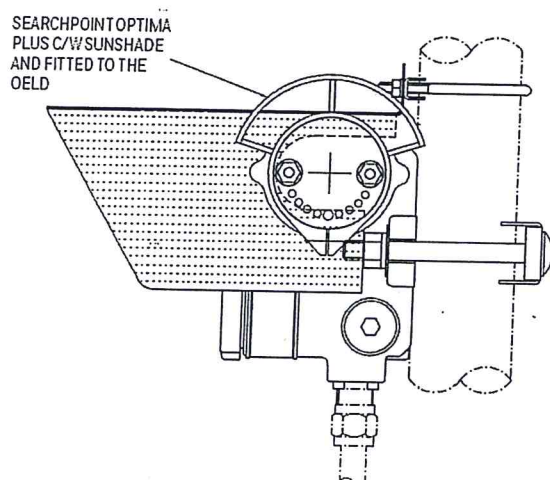2.2.3 Sunshade (94000-A-1006)



A sunshade manufactured from 316 stainless steel, is available which covers the OELD and can extend over either side to also provide protection to a Searchpoint Optima or Searchline Excel

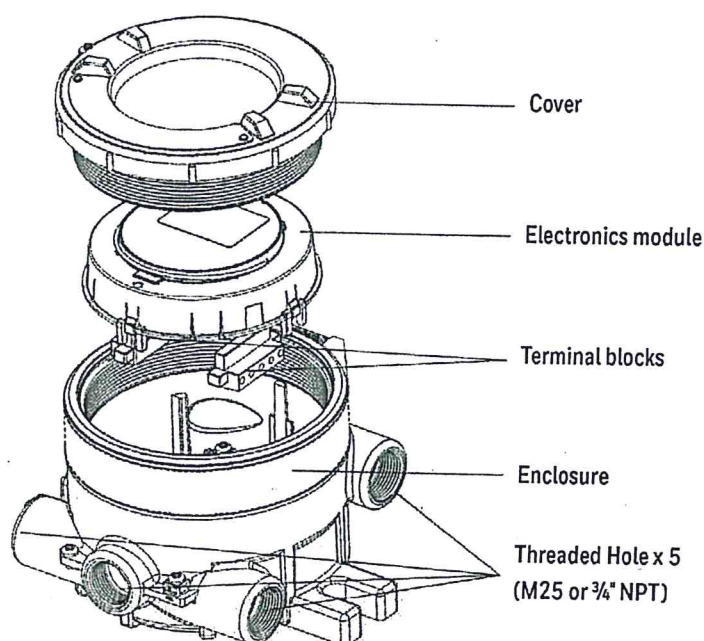
The sunshade slots over the OELD mounting bolts so no additional fixings are required and is stainless steel 316.

Use the sunshade to reduce the effects of direct solar heating.

<Figure 4. OELD with Sunshade>

WARNING

When operating in the hazardous location, ensure that the mobile device being used is suitably certified for that area.




<Figure 1. OELD Exploded View>

2.2 Optional Accessories

Note

The optional pipe mount, ceiling bracket and sunshade accessories are not included as part of the assessment to EN60079-29-1.

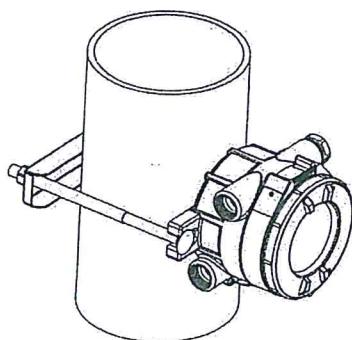2.2.1 Pipe Mount Kit (1226A0358)




<Figure 2. Pipe-Mounted OELD>

The Pipe Mount kit (1226A0358) allows the OELD to be mounted to pipe from 2" to 6" (50 to 150 mm) in diameter. The kit includes the pipe mount bracket, two carriage bolts, nuts, and lock washers.

Digital Linear Heat Detection Cable 88°

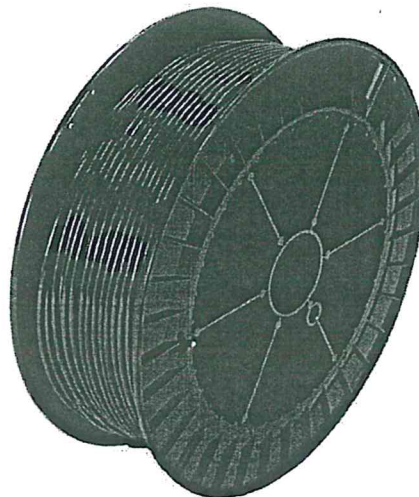with Nylon Armline II Series



Overview

Digital Linear Heat Detection (LHD) cable with a 88°C fixed temperature activation rating has a nylon outer sheath for UV protection and increased durability for external applications. It is available in 100m, 500m and 1,000m lengths.

A range of digital sensor cables provides a very simple fixed temperature heat detection system which can be used in many situations where other forms of detection are not suitable.

Operation

A range of digital LHD cables contains a pair of twisted, distance, tri-metallic conductors sheathed with advanced temperature sensitive polymers. The cable operates by softening and separation of the conductors, the tension of the twisted conductors then causes the two cores to fuse together. The cable provides a simple switch operation which when combined with a combination of end-of-line (EOL) monitoring and trigger resistors can signal an alarm to any fire monitoring system through any monitored input, i.e. conventional detection or addressable interface unit.

Location Control Unit

In addition to the LHD sensor cable, an optional digital location unit which monitors the sensor cable and can identify the length of the sensor cable where an alarm condition has occurred, is also available.

Fixings for all applications

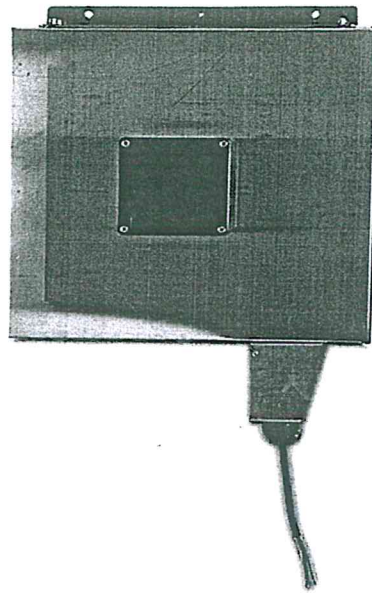
A range of 'edge', 'A', 'P' and 'T' clips allow the cable to be easily installed. The clips provide heat insulation as well as support the cable at the correct distance from cable trays, steel ceilings and walls.

Standard Features

- **CUL/UL 521 approved**
- **FM approved (Class 3210)**
- Up to 3,000m per zone
- Detection along total cable length
- Optional extrusions for different environments
- Simple maintenance free installation
- **Suitable for use in hazardous areas**

Auto Cable Reeler

Armline II Series



Overview

Automatic cable reelers are supplied with an explosion proofarbonate junction box (K241EX) or Stainless Steel junction 247EX). A cable reeler is normally placed on the roof of a floating roof tank structure where it ensures electrical continuity of a linear heat detection (LHD) sensor cable and the fire alarm system during the upward and downward movement of the floating roof. The cable reeler ensures that the cable remains taut and prevents that cable from getting jammed in the moving parts of the roof.

Installation

Mounted on the top rim of a tank body, the cable is connected to a junction box (eg. 1-B6782-190) on the tank roof. The reeler follows the movement of the roof, uncoiling the cable as the roof lowers, and recoiling the cable when the roof rises.


Application

3836-K241EX supports a cable drop of up to 25m. For hazardous areas, suitable safety barriers are required.

Standard Features

- Simplifies electrical connections of floating roof tanks
- Collects and releases cable in moving installations avoiding cable jams
- Supplied with suitable chemical resistant cable
- Flame retardant

1D Cable Accessory - e Wrap & Tool CA-TW/ACA-TWT) rmline II Series



view

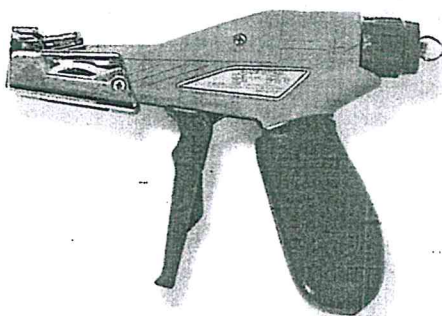
CA-TW series tie wraps (cable ties) are designed to secure heat sensor cable to the LHD brackets and clips. The tie wraps are available in various temperature ratings for matching the temperature specifications of the selected LHD cable.

PA66 and stainless steel variants are suitable for outdoor applications whilst stainless steel variants additionally allow for the installation of very high temperature digital cable.

ACA-TWT is available for the stainless steel tie wrap application.

Stainless Steel Tie Wrap Tool

ACA-TWT is a tie wrap (cable tie) tensioner and cutter for stainless steel cable ties.



Standard Features

Tie Wrap

- Easy installation of linear heat cable
- For use with LHD brackets and clips
- Indoor and outdoor applications
- Available in PA66, ETFE and stainless steel
- Available in quantities of 25 or 100

Tie Wrap Tool (Stainless Steel)

- Easy fitment of stainless steel tie wraps
- Tensioning and cuts

Linear Heat Cable Accessory - Silicone Sleeve (ACA-RS) Formline II Series



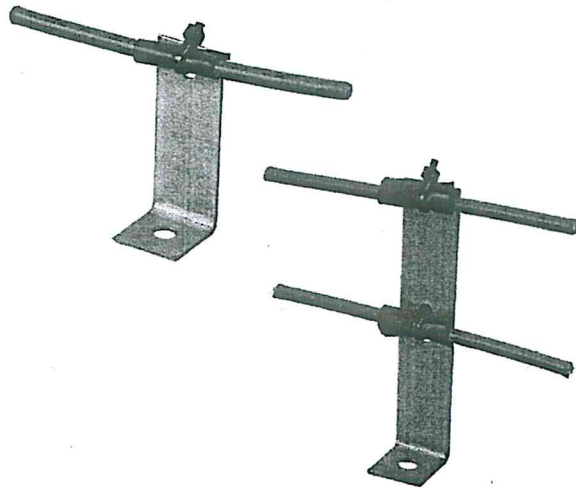
Overview

ACA-RS series silicone sleeves are designed to protect linear heat sensor cable against mechanical damage from the tie wrap when the cable is secured. The ACA-RS is a split sleeve to protect the sensor cable from being crushed or damaged attached to fixing clips or brackets. It acts as an insulator to prevent the transfer of heat through these metal clips or brackets to the LHD cable, and is fire resistant.

Standard Features

- Protection of linear heat cable against mechanical damage
- For use with any LHD fastening brackets or clips
- Fire resistant
- Available in quantities of 25 or 100

HD Cable Accessory - Bracket "L" with Sleeve (ACA-BL) Formline II Series



View

ACA-BL series L-bracket is designed to support linear heat cable above the risk area, eg. the top run of a cable tray. A silicon ion sleeve is supplied with the unit to protect the sensor when fastened to the bracket.

Installation

ACA-BL may be fitted to the cable tray and secured in place suitable bolt and nut at one end. The hole at the other end of bracket allows for the securing of the sensor cable using the sleeve and cable tie. The L-bracket allows support for sensor cable at the selected distance away from the detection


Recommended spacing: 1m.

Standard Features

- Easy installation of linear heat cable
- For use on cable trays
- Available in zintec or stainless steel
- Available in quantities of 25 or 100


A-BL20-025

Cable Accessory - Bracket "L", 200mm (7.9") (Zintec) w/ Sleeve - Qty25







Details


- Easy installation of linear heat cable
- For use on cable trays
- Available in zintec
- Available in quantities of 25



3D VIEW 300W WITH CLP UL38 PCB
0000071 / 0000070



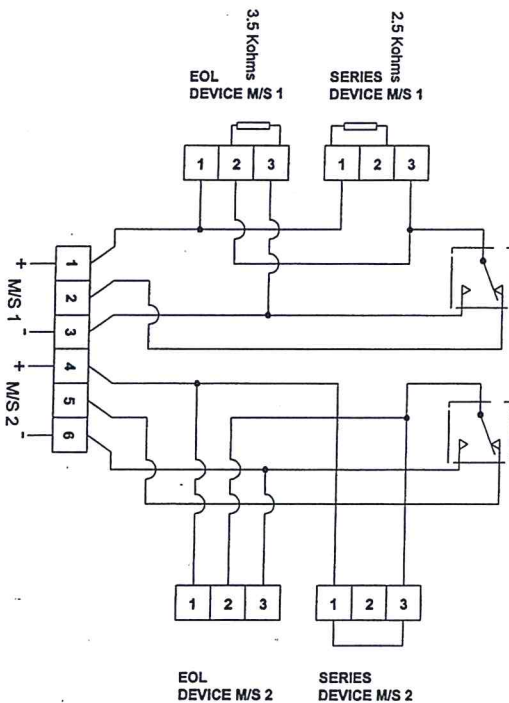ELECTRICAL WIRING
Optional Single or Double Microswitch
Circuit shown with Unit un-operated : GNEKCP7 UL38 PCB
Version M/S 1 M/S 2



NO	REV	DATE	DESCRIPTION
1	1		ISSUED FOR APPROVAL


ABB TURBOCHARGERS

Enppi
ENGINEERING FOR THE PETROLEUM AND
ENRPI PROJECT NUMBER :
SBS-220-175
5333 West Ashburne St Suite 200
Tel: +(1) 832-686-8428
Email: sales@enppi.com

Project Name: EGPC CRUDE O

DRAWING TITLE	DRAWING NUMBER
INSTRUMENT TERMINAL HOOK UP DETAIL	SBS-J08503-DC18-118-011

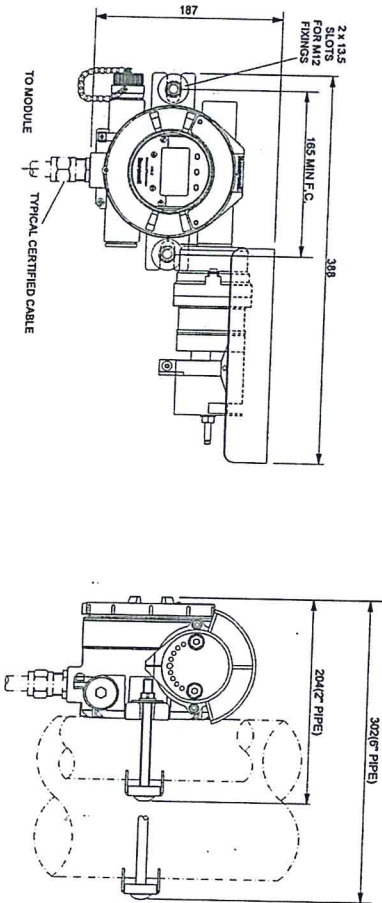COMBUSTIBLE GAS DETECTOR



SIDE VIEW (OPTIONAL 2" & 6" PIPE MOUNTING)

- 2) ELEVATION OF DEVICE SHALL BE AS I SITE CONDITIONS TO FIT THE DEVICE IN FR OF AND AT THE CENTER OF FRESH AIR INT, WITH A DISTANCE OF 30 TO 40 CM AWAY FF IT.
- 3) A DEVICE SHALL BE INSTALLED AS PE NOTE 2 FOR EACH HVAC UNIT.
- 4) MODULE SHALL BE INSTALLED INDOO TO THE WALL BEHIND THE DEVICE.

REV	DATE	DESCRIPTION	PREPARED	CHECKED	APPROVED

الهندسة للمصالح العامة والخاصة
Enppi
ENGINEERING FOR THE PETROLEUM AND PROCESS INDUSTRIES
ENPPI PROJECT NUMBER 4176-503

Project Name: EGPC CRUDE OIL TANK FARM

DRAWING TITLE
INSTRUMENT TERMINATION AND
HOOK UP DETAILS


SCALE	DRAWING NUMBER	SHEET NUMBER	REV:
-------	----------------	--------------	------

FS24X Detector

FS24X is a quantum leap in flame and fire detection with its sophisticated software and detection technology.

The FS24X is the latest generation high technology Multi-Spectrum Triple IR (IR/IR/IR/Visible) Fire and Flame Detector, which is part of our FSX family of advanced technology Electro-Optical fire detectors. Using our patented WideBand IR™, WideBand 4.3 micron IR™, and Visible detection technology, the FS24X is a quantum leap in flame and fire detection. Sophisticated software algorithms and dual microprocessors ensure that the FS24X has the highest fire detection performance combined with optimal false alarm rejection.

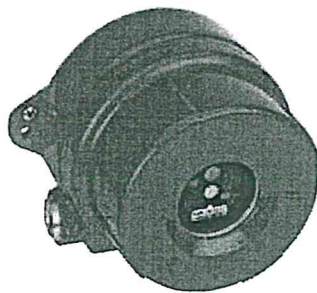
The WideBand IR™ Infrared technology using high-speed solid-state Quantum sensors allows detection of all types of fires, hydrocarbon and non-hydrocarbon, in all weather conditions. If the detector's signal is blocked by ordinary window glass, the patented WideBand IR sensors will still alarm to the fire albeit at a reduced sensitivity and slower response time.



Dual microprocessors provide a high level of fail-safe operation combined with fast and reliable performance. The master microprocessor performs high-speed digital sampling and signal processing calculations, while the slave microprocessor handles various sensor data, performs communications, self-diagnostics and provides interface versatility and additional memory for storing Event Log and FirePic™ data.

The FSX family of detectors feature our patented FirePic data storage and information retrieval facility. FirePic™ records pre-fire data, which can be recovered from the Detector's non-volatile flash memory for post fire analysis and postulation of the fire cause. Additionally, unique Real-Time Graphing (RTG™) allows viewing of the data which the Detector actually sees. A combination of outputs makes the FS24X a truly versatile detector for today's demanding industrial requirement. The FS24X detector has a detection range greater than 60 m (200 feet) (Very High Sensitivity setting) for the detection of a 0.1 m² (one square-foot) Heptane reference fire and has a cone of vision far greater in volumetric coverage than any other Multi-Spectrum IR Detector. This means fewer Detectors can be used as compared to other manufacturers' Detectors.

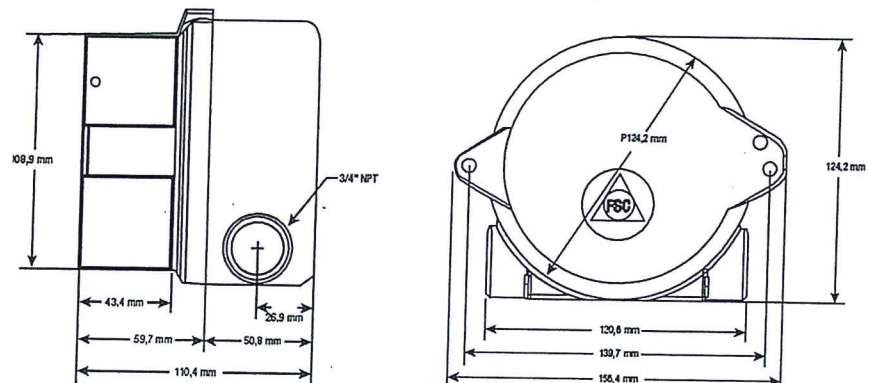GENERAL DIMENSIONS
Side and Back Views
(All Dimensions in mm)



General Specification

GENERAL SPECIFICATIONS	
FIELD OF VIEW	FS24X-9: 90° cone of vision, $\pm 45^\circ$ from on axis FS24X-2: 110° cone of vision, $\pm 55^\circ$ from on axis
SENSITIVITY	Very high (60m), high (45m), medium (30m) and low (15m) - switch selectable
RESPONSE TIME	3-5 Seconds to 0.1 m ² (1 sq. ft.) n-Heptane fire at 30 m (100 ft.) 3-10 Seconds to 0.1 m ² (1 sq. ft.) n-Heptane fire at 60 m (200 ft.)
SPECTRAL SENSITIVITY	Visible: 400 - 700 nanometres Near Band IR: 0.7 - 1.1 microns Wide Band IR: 1.1 - 3.0 microns Wide Band IR: 3.0 - 5.0 microns
OPERATING VOLTAGE	24 Vdc nominal (18-32 Vdc) - regulated
POWER CONSUMPTION	Operating: 56 mA @ 24 Vdc nominal Alarm: 106 mA @ 24 Vdc nominal Heater: 155 mA - additional Note: Heater will turn on at -17°C (0°F)
OUTPUT RELAYS	Fire Alarm: SPDT (NO / NC) - De-energised/energized, latching/non-latching Fault: SPST (NO) - De-energised, latching/non-latching Auxiliary: SPDT (NO / NC) - De-energised/energized, latching/non-latching Contacts rating: 1 amp @ 24 Vdc
ANALOG OUTPUT	0 - 20 mA stepped - source or sink user selectable
LOOP RESISTANCE	50 - 400 Ohms
COMMUNICATION	One of the following - user selectable: • RS-485, ModBus Protocol • RS-485, FireBus II • RS-485 Special (optional) • HART, Optional plug-in module (not available on EN54-10 units)
VISUAL INDICATORS	Green LED: Power Red LED: Alarm Yellow LED: Fault
TEMPERATURE RANGE	Operating: 110° Field of View FS24X: -40°C to +85°C (-40°F to +185°F); 90° Field of View FS24X: -60°C to +85°C (-76°F to +185°F) Storage: -55°C to +110°C (-67°F to +230°F)
HUMIDITY RANGE	5 to 98% relative humidity, non-condensing
VIBRATION	Meets or exceeds MilSpec 810C Method 514.2, Curve AW12
WIRING	2.5 mm ² (14 AWG) to 0.326 mm ² (22 AWG); shielded cable recommended
CONDUIT ENTRIES	Standard: Two M25 or two 3/4" NPT
ENCLOSURE MATERIALS	Copper-free powder coated aluminum or 316 stainless steel
ENCLOSURE TYPE	4X, IP66 and NEMA 4
CERTIFICATIONS	FM: Class I, Div. 1 & 2, Groups B, C, & D; Class II, Div. 1 & 2, Groups E, F, & G; Class III ATEX/IECEx: II 2 G Ex db IIC T4 (Ta: -60 to +110°C), T5 (Ta: -60 to +75°C), T6 (Ta: -60 to +60°C), II 2 D Ex tb IIC T135°C (FS24X-9, 90° Field of View) II 2 G Ex db IIC T4 (Ta: -40 to +110°C), T5 (Ta: -40 to +75°C), T6 (Ta: -40 to +60°C), II 2 D Ex tb IIC T135°C (FS24X-9, 110° Field of View) CE: Complies with EN6100-6-4 & EN50130-4 INMETRO CU-TR SIL Rating: FMEDA available on request EN54-10: FS20X certified 1175a/01 (LPCB); CPR 0832-CPR-F0515
SHIPPING WEIGHT	Aluminum: 1.6 kg (3.6 lbs) Stainless Steel: 3.2 kg (7 lbs)
MOUNTING	Swivel bracket assembly - optional
WARRANTY	Three years from date of shipping

FEATURES

- Patented WideBand IR™ technology
- Patented Electronic Frequency Analysis™
- Visible sensor for optimum false alarm rejection
- Selectable detection sensitivities
- Field-of-View: 110° cone-of-vision (90° cone-of-vision model also available)
- Dual microprocessors for reliable performance
- Real-time clock for accurate time dating of events
- FirePic™ - pre-fire event data storage
- Event log with date and time stamp
- RS-485 ModBus communication
- Non-isolated 4-20 mA Analog output (sink or source)
- Alarm, Fault and Fire Verification relays
- Automatic optical path and electronic self-test
- Patented Electronics Module for component protection with easy plug-in terminations and field installation
- Two 25 mm or 3/4" NPT conduit entries
- Low power consumption
- High RFI and EMI immunity
- FM, ATEX, CE mark approvals
- CU-TR approved
- INMETRO approved
- Meets SIL 2 requirements
- Certified to EN54-10:2002 (FS24X-9) option
- FM 3260 Performance


BENEFITS

- Detects hydrocarbon and non-hydrocarbon fuel fires in all environmental conditions
- User selectable outputs
- Wide operating temperature range
- Optimal false alarm rejection
- Minimal maintenance for trouble-free operation
- PC software and Interface Module (FSiM) for fault diagnostics, real-time graphics (RTGs), and downloading of FirePics™ and event log
- Suitable for a wide variety of applications
- Easy electronics module replacement
- Test lamps for manual testing

APPLICATIONS

- Refineries and oil production facilities
- Off-shore platforms
- Turbine/Compressor enclosures
- Oil and gas pipelines and pumping stations
- LNG/LPG loading and unloading facilities
- Natural gas and CNG plants
- Ethanol, Methanol, and IPA production and storage
- Crude oil and gasoline storage and tank farms
- Aircraft hangars
- Paint and solvent storage
- Chemical production, storage, and loading facilities
- Power plants

Technical Summary




Searchpoint Optima Plus Specification

Measuring Range	0-100% LEL, wide selection of Hydrocarbon gas and vapour calibrations. Different measuring ranges and solvent calibrations available for specialist applications	
Signal Output	4-20mA autosensing sink or source	
Inhibit	1-3mA (Default 2mA)	
Warning	0-6mA (Default 3mA *)	
Fault	0mA (HART® units adjustable to 1mA)	
Over Range	20-21.5mA (Default 21mA)	
Digital Output	Optional Multidrop Modbus RS485 (via XNX, Optional HART® over 4-20mA output (HART® version 7)	
Material	316 stainless steel	
Weight	1.6kg	
Accuracy		
Optima Plus (Hydrocarbon)	Baseline < +1% FSD, 50% FSD < ±2% FSD	
Optima Plus (Ethylene)	Baseline < ±2% FSD, 50% FSD < ±3% FSD	
Repeatability	< ±2% FSD at 50% FSD	
Linearity	< 5% FSD	
Response Time	T50 < 3 seconds, T90 < 4 seconds (methane)	
Operational and Certified**	-40°C to +65°C temperature range **CU-TR-EX (Russia) Approval - XTC Version, Certified Temperature Range -60°C to +65°C	
Long Term Stability (as defined in EN 60079-29-1)	Baseline	Methane 100 %LEL Range: $\leq \pm 2\%$ FSD Ethylene 100 %LEL Range: $\leq \pm 4\%$ FSD
	50 %FSD	Methane 100 %LEL Range: $\leq \pm 4\%$ FSD Ethylene 100 %LEL Range: $\leq \pm 5\%$ FSD
Drift Over Temperature Range (-40 °C to 65 °C)	Baseline	$\leq \pm 2\%$ FSD
	50 %FSD	Methane 100 %LEL Range: $\leq \pm 0.131\%$ FSD per °C Ethylene 100 %LEL Range: $\leq \pm 0.078\%$ FSD per °C
Variation with Pressure	0.1% (of reading) per mbar	
Power Supply	18-32Vdc (24Vdc nom), < 4.5W max	
Environmental Protection	IP 66 / 67	
Diagnostics (and Re-calibration)	Via certified Hand-held Interrogator, XNX or optional HART® communications	
Safety Approvals	ATEX: Bassefa13ATEX0296X II 2 GD Ex d op is IIC Gb Ex Ib IIC Db T96°C (T _{amb} -40°C to +65°C) T86°C (T _{amb} -40°C to +55°C) IP 66/67 UL / CSA: Class 1, Div 1, groups B, C, and D (-40°C to +65°C) IECEx: II 2 GD Ex d op is IIC Gb Ex Ib IIC Db T86°C (T _{amb} -40°C to +55°C) or T96°C (T _{amb} -40°C to +65°C) IP66/67 CU-TR-EX (Russian Customs Union) - XTC Version 1Ex d op is IIC T5/T4 Gb X (T _{amb} -60°C to +65°C)	
Performance Approvals	EN 60079-29-1 (BVS 03 ATEX G 016 X), CSA C22.2 152, FM ANSUSA-12.13.01., Russian Pattern Approval (Metrology) - XTC Version ***	
Functional Safety	IEC61508 Safety Integrity Level 2	
EMC Compliance	EN 50270:2006	
Software	EN 50271:2010	
Marine Approvals	Marine Equipment Directive (MED), type approvals from DNV, BV, ABS, Lloyd's Register	

* Note for ATEX compliance the warning value should not be set between 3 and 5mA
*** Please refer to manual for full information

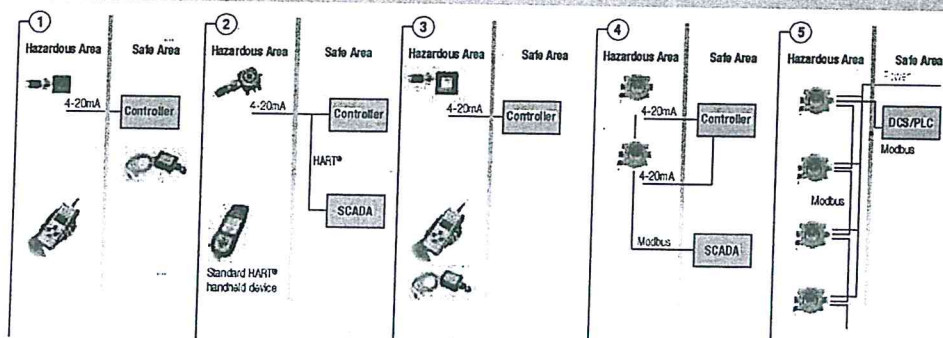Installation Options



® POTTER
The Symbol of Protection



PS10 SERIES PRESSURE SWITCH

[illegible]

Installation

amper
over incorporates tamper resistant fastener that requires a special key for removal. One key is supplied with each device. For optional cover tamper
which kit, order Stock No. 0090200. See bulletin #5401200 PSCISK.


Ordering Information	
Model	Description
PS10-1	Pressure switch with one set SPDI contacts
PS10-2	Pressure switch with two sets SPDI contacts
	Hx Key
	Cover Tamper Switch Kit
Stock No.	5250062
	0090200

(DO NOT USE PIPE DOPE)
The device should be mounted in the right position (indicated connection down).
Remove the tamper resistant screw with the special key provided.
Carefully place a screwdriver on the edge of the knockout and sharply apply a force sufficient to dislodge the knockout plug. See Fig 9
Run wires through an approved conduit connector and attach the connector to the device.
Connect the wires to the appropriate terminal connections for the service intended. See Figures 2,4,5, and 6. See Fig 7 for two switch, one conduit wiring.
Installation
The operation of the pressure alarm switch should be tested upon completion of installation and periodically thereafter in accordance with the applicable NFPA codes and standards and/or the authority having jurisdiction.
System:
When used with PS10 and control unit with retard - connect PS10 to PS10.


Her Electric Signal Company, LLC • St. Louis, MO • Phone: 866-956-0988/Canada 888-882-1833 • www.politersignal.com

**PS10 SERIES
PRESSURE SWITCH**

Fig. 1
Switch Clamping Plate Terminal




WARNING
An uninsulated section of a single conductor should not be looped around the terminal and must be severed, thereby providing supervision of the connection in the event that the wire becomes dislodged from under the terminal.



NOTE: To prevent leakage, apply Teflon tape sealant to male thread only.


DWG 930-1

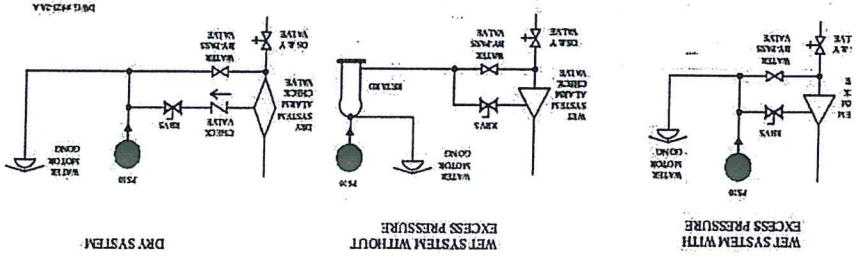Typical Sprinkler Applications



CAUTION

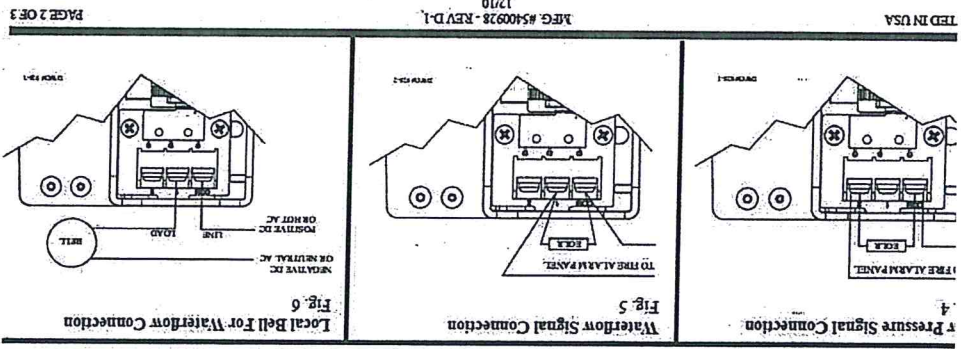Closing of any shutoff valves between the alarm check valve and the PS10 will render the PS10 inoperative. To comply with NFPA-72 any such valve shall be electrically supervised with a supervisory switch such as Potter Model RBVS.



TEST IN USA

REF: #540928 - REV D-1
12/10

PAGE 2 OF 3


PS10 SERIES PRESSURE SWITCH

POTTER


The Symbol of Protection

e Conduit Wiring


It cut this section of divider to provide path for wires
in wiring both switches from one conduit entrance.



Switch Operation

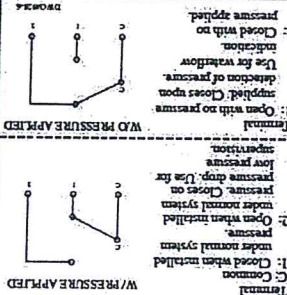

Removing Knockouts



CAUTION

Do not tighten by grasping the switch enclosure. Use wrenching flats on the bushing only. Failure to install properly could damage the switch and cause improper operation resulting in damage to equipment and property.
To seal threads, apply Teflon tape to male threads only. Using joint compounds or cement can obstruct the pressure port inlet and result in improper device operation and damage to equipment.
Do not over tighten the device, standard piping practices apply.

WARNING

Installation must be performed by qualified personnel and in accordance with all national and local codes and ordinances. Shock hazard. Disconnect power source before servicing. Read all instructions carefully and understand them before using installation. Save instructions for future use. Failure to read and understand instructions could result in improper operation of device resulting in serious injury or death. Risk of explosion. Not for use in hazardous locations. Serious injury or death could result.

Pressure Switch

Pressure switch shall be a Model PS10 as fabricated by Potter Electric Signal Company, St. Louis MO. It shall be installed on the fire sprinkler system as shown and or listed herein.
It shall be provided with a 1/2" NPT male pressure connection and be connected to the alarm port outlet of Wet Pipe Alarm Valves, Dry Pipe Valves, Pre-Action Valves, or Deluge Valves. The switch shall be actuated when the alarm line pressure reaches 10.1 (0.27 - 0.55 BAR).
The type waterflow switches shall have a maximum service rating of 300 PSI (20.68 BAR) and shall be factory adjusted rate on a pressure increase of 4 - 8 PSI (0.27 - 0.55 BAR).

Pressure switch shall have one or two form C contacts, switch contact rating 10.1 Amps at 125/250 VAC, 2.0 Amps at 30 VDC.
Pressure type waterflow switches shall have two conduit entrances one for each individual switch compartment to facilitate the use of dissimilar voltages for each individual switch.
The cover of the pressure type waterflow switch shall be Zinc die-cast with rain lip and shall attach with one tamper resistant screw. The pressure type waterflow switch shall be suitable for indoor or outdoor service with a NEMA 4/IP66 rating.
The pressure type waterflow switch shall be UL, UIC and CSFM listed. FM and LPC approved and NEMA 4 accepted.

FIG. 8

12/10

PAGE 3 OF 3

UNITED STATES



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

12.03- Motor Datasheets



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

12.04- Electrical Cables Schedule

ITEM	CABLE TAG	CABLE COMPOSITION mm ²	SIGNAL TYPE	SHIELDING		ARM.	FROM	TO	LENGTH (m)	EXT. COLOUR SHEATH	EXT. DIA. (mm)	GLAND TYPE (NOTE-2)	DRUM NO.	CABLE CODE	NOTE	Rev
				Overall	Indiv.											
6	000D002	1 X 3 X 2.5 mm ²	AI		YES	YES	000G002	000J070	420	RED	17.53	PA901-M20	CD-000-F5-02	F6		2
7	000D004	1 X 3 X 2.5 mm ²	AI		YES	YES	000G004	000J070	910	RED	17.53	PA901-M20	CD-000-F6-03	F6		2
8	000D004	1 X 3 X 2.5 mm ²	AI		YES	YES	000G004	000J070	910	RED	17.53	PA901-M20	CD-000-F6-03	F6		2
9	000D005	1 X 3 X 1.5 mm ²	AI		YES	YES	000G005	000J070	20	RED	16	PA901-M20	CD-000-F5-01	F5		2
10	000D006	1 X 3 X 1.5 mm ²	AI		YES	YES	000G006	000J070	20	RED	16	PA901-M20	CD-000-F5-01	F5		2
11	000D007	12 X 3 X 1.5 mm ²	ANALOG	YES	YES	YES	000G007	MARSHALLING CABINET	400	RED	41.4	PA902-M20	CD-000-F1-01	F11		2
1	000D013	1 X 3 X 1.5 mm ²	AI		YES	YES	000G013	000J070	130	RED	16	PA901-M20	CD-000-F5-01	F5		2
2	000D015	1 X 3 X 1.5 mm ²	AI		YES	YES	000G015	000J070	130	RED	16	PA901-M20	CD-000-F5-01	F5		2
3	000D006	1 X 3 X 1.5 mm ²	AI		YES	YES	000G006	000J070	80	RED	16	PA901-M20	CD-000-F5-01	F5		2
4	000D009	1 X 3 X 1.5 mm ²	AI		YES	YES	000G009	000J070	50	RED	16	PA901-M20	CD-000-F5-01	F5		2
5	000D010	1 X 3 X 1.5 mm ²	AI		YES	YES	000G010	000J070	40	RED	16	PA901-M20	CD-000-F5-01	F5		2
6	000D007	1 X 3 X 1.5 mm ²	AI		YES	YES	000G007	000J070	80	RED	16	PA901-M20	CD-000-F5-01	F5		2
7	000D008	1 X 3 X 1.5 mm ²	AI		YES	YES	000G008	000J070	20	RED	16	PA901-M20	CD-000-F5-01	F5		2
8	000D005	1 X 3 X 1.5 mm ²	AI		YES	YES	000G005	000J070	80	RED	16	PA901-M20	CD-000-F5-01	F5		2
9	000D006	1 X 3 X 1.5 mm ²	AI		YES	YES	000G006	000J070	80	RED	16	PA901-M20	CD-000-F5-01	F5		2
12	000J070	12 X 3 X 1.5 mm ²	ANALOG	YES	YES	YES	000J070	MARSHALLING CABINET	400	RED	41.4	PA902-M20	CD-000-F1-02	F11		2
1	000D010	1 X 3 X 1.5 mm ²	AI		YES	YES	000G010	000J070	80	RED	16	PA901-M20	CD-000-F5-01	F5		2
2	000D011	1 X 3 X 1.5 mm ²	AI		YES	YES	000G011	000J070	120	RED	16	PA901-M20	CD-000-F5-01	F5		2
3	000D008	1 X 3 X 1.5 mm ²	AI		YES	YES	000G008	000J070	30	RED	16	PA901-M20	CD-000-F5-01	F5		2
4	000D013	1 X 3 X 1.5 mm ²	AI		YES	YES	000G013	000J070	90	RED	16	PA901-M20	CD-000-F5-01	F5		2
5	000D014	1 X 3 X 1.5 mm ²	AI		YES	YES	000G014	000J070	110	RED	16	PA901-M20	CD-000-F5-01	F5		2
6	000D011	1 X 3 X 1.5 mm ²	AI		YES	YES	000G011	000J070	20	RED	16	PA901-M20	CD-000-F5-01	F5		2
7	000D012	1 X 3 X 1.5 mm ²	AI		YES	YES	000G012	000J070	70	RED	16	PA901-M20	CD-000-F5-01	F5		2
8	000D012	1 X 3 X 1.5 mm ²	AI		YES	YES	000G012	000J070	120	RED	16	PA901-M20	CD-000-F5-01	F5		2
9	000D009	1 X 3 X 1.5 mm ²	AI		YES	YES	000G009	000J070	50	RED	16	PA901-M20	CD-000-F5-01	F5		2
14	000F06	4 X 2 X 1.5 mm ²	DIGITAL	YES	NO	YES	000F06	MARSHALLING CABINET	220	RED	23.2	PA902-M20	CD-000-F7-01	F7		2
15	000F06	4 X 2 X 1.5 mm ²	DIGITAL	YES	NO	YES	000F06	MARSHALLING CABINET	220	RED	23.2	PA902-M20	CD-000-F7-01	F7		2
16	000F06	4 X 2 X 1.5 mm ²	DIGITAL	YES	NO	YES	000F06	MARSHALLING CABINET	220	RED	23.2	PA902-M20	CD-000-F7-02	F7		2
17	000F06	4 X 2 X 1.5 mm ²	DIGITAL	YES	NO	YES	000F06	MARSHALLING CABINET	220	RED	23.2	PA902-M20	CD-000-F7-02	F7		2
18	000F06	4 X 2 X 1.5 mm ²	DIGITAL	YES	NO	YES	000F06	MARSHALLING CABINET	220	RED	23.2	PA902-M20	CD-000-F7-02	F7		2
19	000F06	4 X 2 X 1.5 mm ²	DIGITAL	YES	NO	YES	000F06	MARSHALLING CABINET	220	RED	23.2	PA902-M20	CD-000-F7-02	F7		2
20	000F06	4 X 2 X 1.5 mm ²	DIGITAL	YES	NO	YES	000F06	MARSHALLING CABINET	220	RED	23.2	PA902-M20	CD-000-F7-02	F7		2
21	000F06	4 X 2 X 1.5 mm ²	DIGITAL	YES	NO	YES	000F06	MARSHALLING CABINET	220	RED	23.2	PA902-M20	CD-000-F7-02	F7		2
22	000F06	4 X 2 X 1.5 mm ²	DIGITAL	YES	NO	YES	000F06	MARSHALLING CABINET	220	RED	23.2	PA902-M20	CD-000-F7-02	F7		2
23	000F06	4 X 2 X 1.5 mm ²	DIGITAL	YES	NO	YES	000F06	MARSHALLING CABINET	220	RED	23.2	PA902-M20	CD-000-F7-02	F7		2
24	SUB-SAC	1 X 2 X 1.5 mm ²	DIGITAL	NO	NO	NO	FACT	INPUT DEVICES	1000	RED	11.81					2
25	SUB-SAC	1 X 2 X 1.5 mm ²	DIGITAL	NO	NO	NO	FACT	OUTPUT DEVICES	1000	RED	11.81					2
26	PLC	802X1.5 mm ²	DIGITAL	YES	NO	NO	FACT	PLC	45	RED	29.2	PA902-M22				2
27	PLC	1 X 2 X 1.5 mm ²	DO	NO	NO	NO	FACT	PLC	45	RED	11.81					2
28	ESD	1 X 2 X 1.5 mm ²	DO	NO	NO	NO	FACT	ESD	20	RED	11.81					2
29	HMI	1 X 2 X 1.5 mm ²	SERIAL	NO	NO	NO	FACT	WORKSTATION	25	RED	11.81					2
30	BAT-CHARG	1 X 2 X 1.5 mm ²	DO	NO	NO	NO	FACT	BATTERY CHARGER	70	RED	11.81					2
31	000S010	1 X 2 X 1.5 mm ²	DO	NO	NO	YES	FACT	FACT	220	RED	15.2	PA901-M20	CD-000-F1-01	F1		2
32	000S010	1 X 2 X 1.5 mm ²	DO	NO	NO	YES	FACT	FACT	220	RED	15.2	PA901-M20	CD-000-F1-01	F1		2
33	GATE-SAC	1 X 2 X 1.5 mm ²	DIGITAL	NO	NO	NO	FACT	INPUT DEVICES	40	RED	16.7					2
34	GATE-SAC	1 X 2 X 1.5 mm ²	DIGITAL	NO	NO	NO	FACT	OUTPUT DEVICES	40	RED	16.7					2
35	000S010A	1 X 2 X 1.5 mm ²	DIGITAL	NO	NO	NO	FACT	INPUT DEVICES	30	RED	13.1					2
36	000S010B	1 X 2 X 1.5 mm ²	DIGITAL	NO	NO	YES	FACT	OUTPUT DEVICES	10	RED	15.2	PA901-M20	CD-000-F3-03	F3		2
37	000S010C	1 X 2 X 1.5 mm ²	DIGITAL	NO	NO	YES	FACT	OUTPUT DEVICES	10	RED	15.2	PA901-M20	CD-000-F3-03	F3		2
38	000S010D	1 X 2 X 1.5 mm ²	DIGITAL	NO	NO	YES	FACT	OUTPUT DEVICES	10	RED	15.2	PA901-M20	CD-000-F3-03	F3		2
39	000S010E	1 X 2 X 1.5 mm ²	DIGITAL	NO	NO	YES	FACT	OUTPUT DEVICES	10	RED	15.2	PA901-M20	CD-000-F3-03	F3		2
40	000S010F	1 X 2 X 1.5 mm ²	DIGITAL	NO	NO	YES	FACT	OUTPUT DEVICES	10	RED	15.2	PA901-M20	CD-000-F3-03	F3		2
41	000S010G	1 X 2 X 1.5 mm ²	DIGITAL	NO	NO	YES	FACT	OUTPUT DEVICES	10	RED	15.2	PA901-M20	CD-000-F3-03	F3		2
42	000S010H	1 X 2 X 1.5 mm ²	DIGITAL	NO	NO	YES	FACT	OUTPUT DEVICES	10	RED	15.2	PA901-M20	CD-000-F3-03	F3		2
43	000S010I	1 X 2 X 1.5 mm ²	DIGITAL	NO	NO	YES	FACT	OUTPUT DEVICES	10	RED	15.2	PA901-M20	CD-000-F3-03	F3		2
44	000S010J	1 X 2 X 1.5 mm ²	DIGITAL	NO	NO	YES	FACT	OUTPUT DEVICES	10	RED	15.2	PA901-M20	CD-000-F3-03	F3		2
45	000S010K	1 X 2 X 1.5 mm ²	DIGITAL	NO	NO	YES	FACT	OUTPUT DEVICES	10	RED	15.2	PA901-M20	CD-000-F3-03	F3		2
46	000S010L	1 X 2 X 1.5 mm ²	DIGITAL	NO	NO	YES	FACT	OUTPUT DEVICES	10	RED	15.2	PA901-M20	CD-000-F3-03	F3		2

TERMINAL STRIP :	0	SIGNAL TYPE :	DI/DO	MULTI CABLE TAG :	030IBR02	REG PANEL LOCATION :	SUBSTATION BUILDING	INTERCONNECTING WIRING DIAGRAM FOR JUNCTION BOX
AREA DESCRIPTION :	0	INDIVIDUAL CABLE CODE :	F3.1.4	MULTI CABLE SIZE :	8 X 2 X 1.5 mm ²	UGS CABLE No. :	FGS-MC-01	
JUNCTION BOX TAG :	030IBR02			MULTI CABLE CODE :	030IBR02	TERMINAL STRIP :	030IBR02	

030P5H008	WH	+1	WH	1
	BLACK	-2	BLACK	2
030P5H002	WH	+3	WH	3
	BLACK	-4	BLACK	4
030SV01	WH	+5	WH	5
	BLACK	-6	BLACK	6
030P5H004	WH	+7	WH	7
	BLACK	-8	BLACK	8
030P5H009	WH	+9	WH	9
	BLACK	-10	BLACK	10
030P5H006	WH	+11	WH	11
	BLACK	-12	BLACK	12
SPARE	WH	+13	WH	13
	BLACK	-14	BLACK	14
SPARE	WH	+15	WH	15
	BLACK	-16	BLACK	16

1	WH	-1	WH	1
	BLACK	-2	BLACK	2
2	WH	+3	WH	3
	BLACK	-4	BLACK	4
3	WH	+5	WH	5
	BLACK	-6	BLACK	6
4	WH	+7	WH	7
	BLACK	-8	BLACK	8
5	WH	+9	WH	9
	BLACK	-10	BLACK	10
6	WH	+11	WH	11
	BLACK	-12	BLACK	12
7	WH	+13	WH	13
	BLACK	-14	BLACK	14
8	WH	+15	WH	15
	BLACK	-16	BLACK	16

SHIELD
ARMOUR

030IBR02

TO DIRTY
EARTH
CLEAN EARTH

TO BOX GND SAFETY BOLT
TO DIRTY EARTH
NETWORK

FIRE AND GAS SYSTEM JUNCTION BOX LOCATED FIELD

MULTI CABLE RUN FROM JUNCTION BOX TO PANEL

FIRE AND GAS SYSTEM PANEL

NOTE

THIS DRAWING HAS NOT BEEN REVISED AS IT IS NOT A PROPERTY OF EPC. IT IS THE PROPERTY OF THE CLIENT. THE CLIENT IS RESPONSIBLE FOR THE CORRECTNESS OF THE DATA AND THE INFORMATION PROVIDED. THE CLIENT IS RESPONSIBLE FOR THE CORRECTNESS OF THE DATA AND THE INFORMATION PROVIDED. THE CLIENT IS RESPONSIBLE FOR THE CORRECTNESS OF THE DATA AND THE INFORMATION PROVIDED.



لوجو الشركة العامة للغاز والكهرباء
EGPC
مختصون في تصميم وتركيب وصيانة
الخطوط لنقل الغاز والكهرباء


CRUDE OIL TANK FARM

FIRE AND GAS INTERCONNECTING WIRING DIAGRAM

DRAWING NUMBER :	SCALE :	SHEET :	REV :
030P5H008-001	1/1	2	2

TERMINAL STRIP :		0		SIGNAL TYPE :		DU/DO		MULTI CABLE TAG :		030UB05		F&G PANEL LOCATION :		SUBSTATION BUILDING		INTERCONNECTING WIRING DIAGRAM FOR JUNCTION BOX	
AREA DESCRIPTION :		0		INDIVIDUAL CABLE CODE :		F3.14		MULTI CABLE SIZE :		8 X 2 X 2.5 mm ²		F&G CABINET No. :		FGS-MC-01		030UB05	
JUNCTION BOX TAG :		030UB05						MULTI CABLE CODE :		F3		TERMINAL STRIP :		030UB05			

030MCP006	WH	1	WH	1
	BLACK	2	BLACK	2
030UH008	WH	3	WH	3
	BLACK	4	BLACK	4
030UH007	WH	5	WH	5
	BLACK	6	BLACK	6
030STB007	WH	7	WH	7
	BLACK	8	BLACK	8
030H007	WH	9	WH	9
	BLACK	10	BLACK	10
030ST007	WH	11	WH	11
	BLACK	12	BLACK	12
SPARE	WH	13	WH	13
	BLACK	14	BLACK	14
030PSH007	WH	15	WH	15
	BLACK	16	BLACK	16

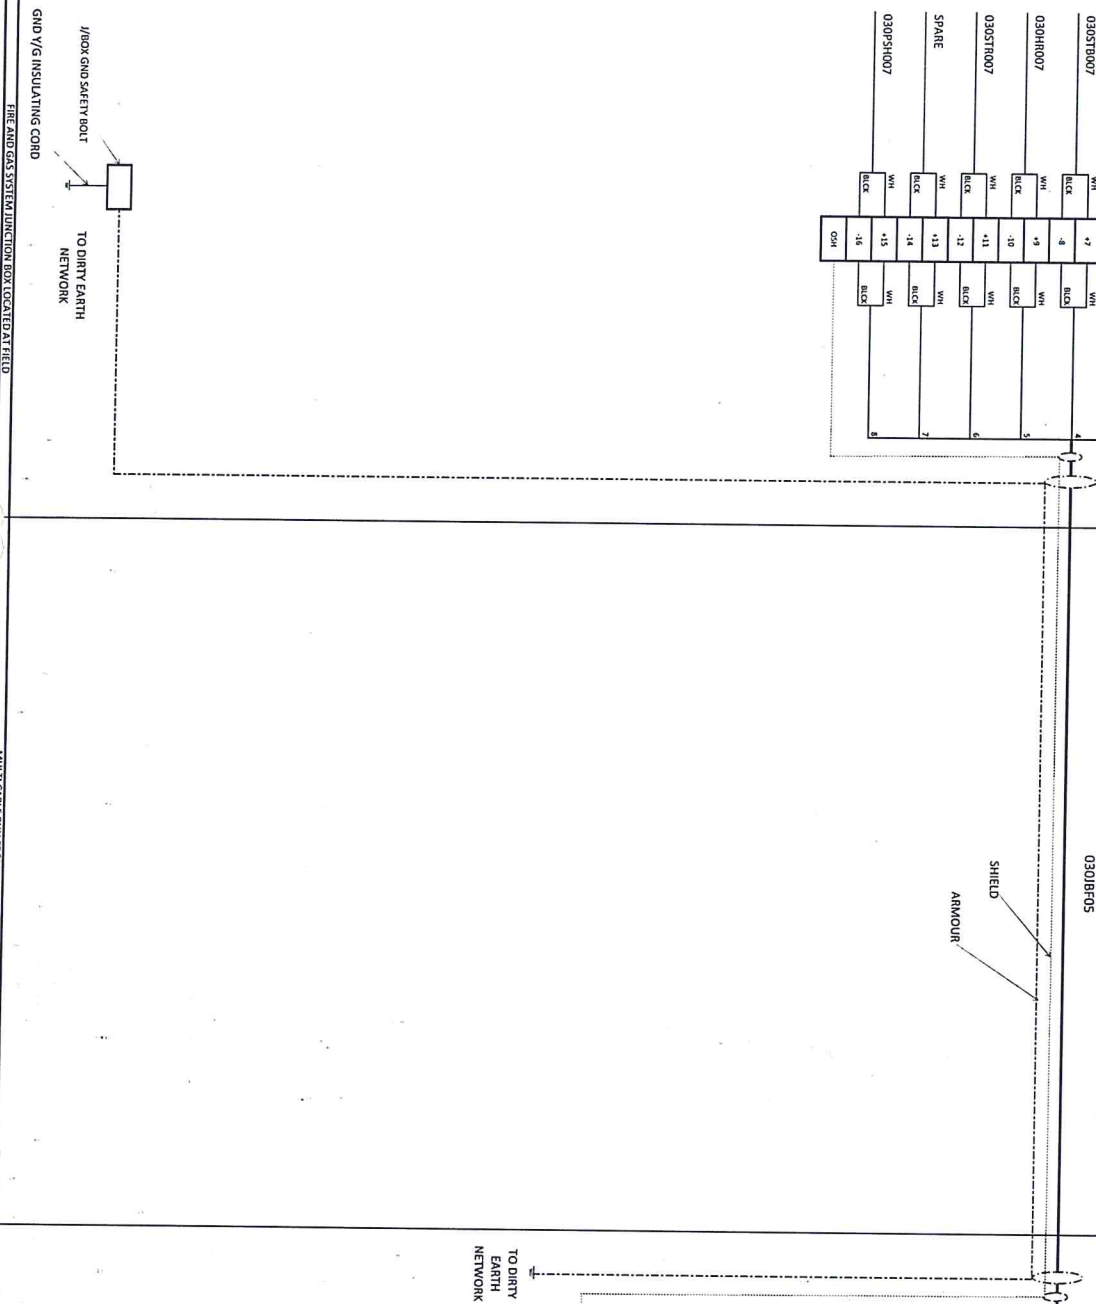

1	WH	1	WH	1
2	BLACK	2	BLACK	2
3	WH	3	WH	3
4	BLACK	4	BLACK	4
5	WH	5	WH	5
6	BLACK	6	BLACK	6
7	WH	7	WH	7
8	BLACK	8	BLACK	8
9	WH	9	WH	9
10	BLACK	10	BLACK	10
11	WH	11	WH	11
12	BLACK	12	BLACK	12
13	WH	13	WH	13
14	BLACK	14	BLACK	14
15	WH	15	WH	15
16	BLACK	16	BLACK	16




Abb.	Description
JIB	DIGITAL JUNCTION BOX
AMP	ANALOG JUNCTION BOX
RD	RED WIRE COLOR
WH	WHITE WIRE COLOR
BC	BLACK WIRE COLOR
UD	UNIDIRECTIONAL DETECTOR
MC	MANUAL CALL POINT
PSH	PRESSURE SWITCH HIGH
HR	HORN
STR	RED STROBE
STR	RED STROBE
SV	SOLENOID VALVE CONTROLLER SIGNAL
GD	ANALOG GAS DETECTOR
FD	FLAME DETECTOR

NOTICE

THIS DRAWING WAS NOT REVISIONED. IT IS THE SOLE PROPERTY OF EGPCC. IT IS TO BE USED ONLY FOR THE PROJECT AND NOT FOR ANY OTHER PROJECT. THE EGPCC PROJECTS ARE NOT TO BE REPRODUCED OR COPIED IN ANY FORM OR BY ANY MEANS, ELECTRONIC OR MECHANICAL, INCLUDING PHOTOCOPYING, RECORDING, OR BY ANY INFORMATION STORAGE AND RETRIEVAL SYSTEM, WITHOUT PERMISSION IN WRITING FROM EGPCC. ANY VIOLATION OF THIS NOTICE WILL BE PROSECUTED TO THE MAXIMUM OF THE LAW.



الهيئة العامة للغازات والنفط
EGPC
مختبر الغازات والنفط
EGPC


CRUDE OIL TANK FARM

FIRE AND GAS INTERCONNECTING WIRING DIAGRAM


DRAWING NUMBER: 02511-1003-0001

SCALE: SHEET 2 OF 2
DATE: 2017-07-27

TERMINAL STRIP:	0	SIGNAL TYPE:	AI	MULTI CABLE TAG:	030ABT01	FIELD PANEL LOCATION:	SUBSTATION BUILDING	INTERCONNECTING WIRING DIAGRAM FOR JUNCTION BOX
AREA DESCRIPTION:	0	INDIVIDUAL CABLES CODE:	FS/6	MULTI CABLE SIZE:	12 x 3 x 2.5 mm ²	WIRING CABINET No.:	REG-SAC-01	
JUNCTION BOX TAG:	030ABT01			MULTI CABLE CODE:	F12	TERMINAL STRIP:	030ABT01	

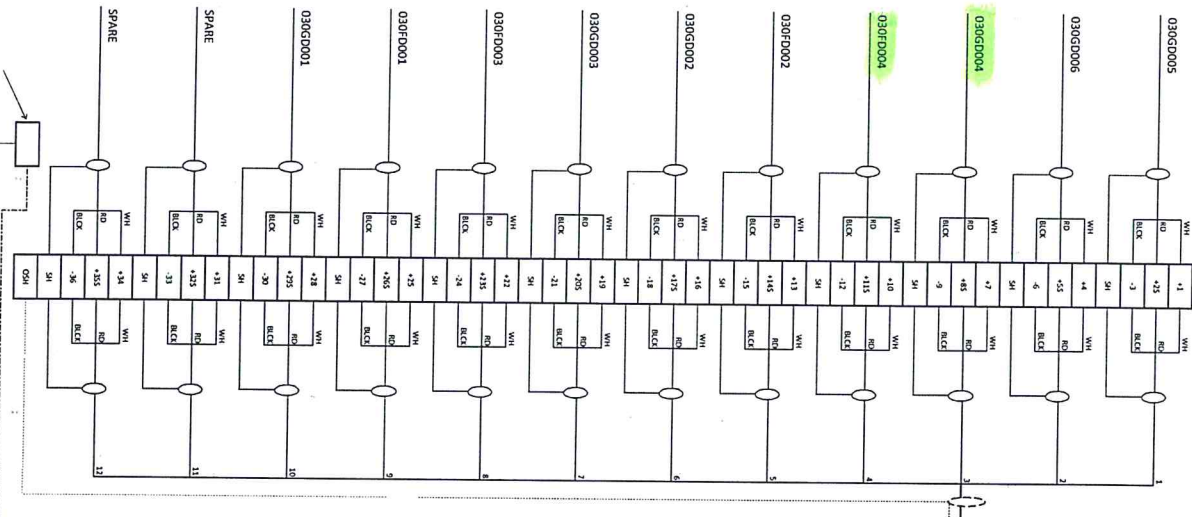

030ABT01
SHIELD
ARMOUR




TO DIRTY EARTH
CLEAN EARTH
NETWORK

Abb.	DESCRIPTION
ABT	TERMINAL STRIP
ABT	ANALOG JUNCTION BOX
NO	NEUTRAL WIRE COLOR
WH	WHITE WIRE COLOR
BL	BLACK WIRE COLOR
LD	LINE NEUTRAL DETECTION
MD	MANUAL CALL POINT
PS	PRESSURE SWITCH HIGH
PH	PHASE
STB	RED STOP
STB	RED STOP
SV	SCALING VALVE OUTPUT SIGNAL
GD	ANALOG GAS DETECTION
FD	FLAME DETECTION

NOTICE

THE DRAWING IS THE PROPERTY OF EGPCC. IT IS TO BE USED FOR THE PROJECT ONLY AND NOT TO BE REPRODUCED, COPIED, LOANED, OR OTHERWISE DISCLOSED TO ANY OTHER PARTY WITHOUT THE WRITTEN PERMISSION OF EGPCC. ANY VIOLATION OF THIS NOTICE SHALL BE CONSIDERED A BREACH OF CONTRACT AND SUBJECT TO LEGAL ACTION.



EGPC	CRUDE OIL TANK FARM
THE AND GAS INTERCONNECTING WIRING DIAGRAM	
DRAWING NUMBER:	0121-1000-00000000
SCALE	SHEET
1:1	2
REV	2




Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

12.05- Electrical Cables Laying Certificates

Area No.	REC No.	No. of layers	no. sheets per layer	length (m)	width	height	BOC Level
030	FRIC 01	1	2	8	500	300	850
	FRIC 02	1	2	8	500	300	850
	FRIC 03	1	2	23	500	300	850
	FRIC 04	1	2	8	500	300	850
	FRIC 05	1	2	8	500	300	850
	FRIC 06	1	2	10	500	300	850
	FRIC 07	1	2	23	500	300	850
	FRIC 08	1	2	8	500	300	850
	FRIC 09	1	2	8	500	300	850
	FRIC 10	1	2	23	500	300	850
	FRIC 11	1	2	8	500	300	850

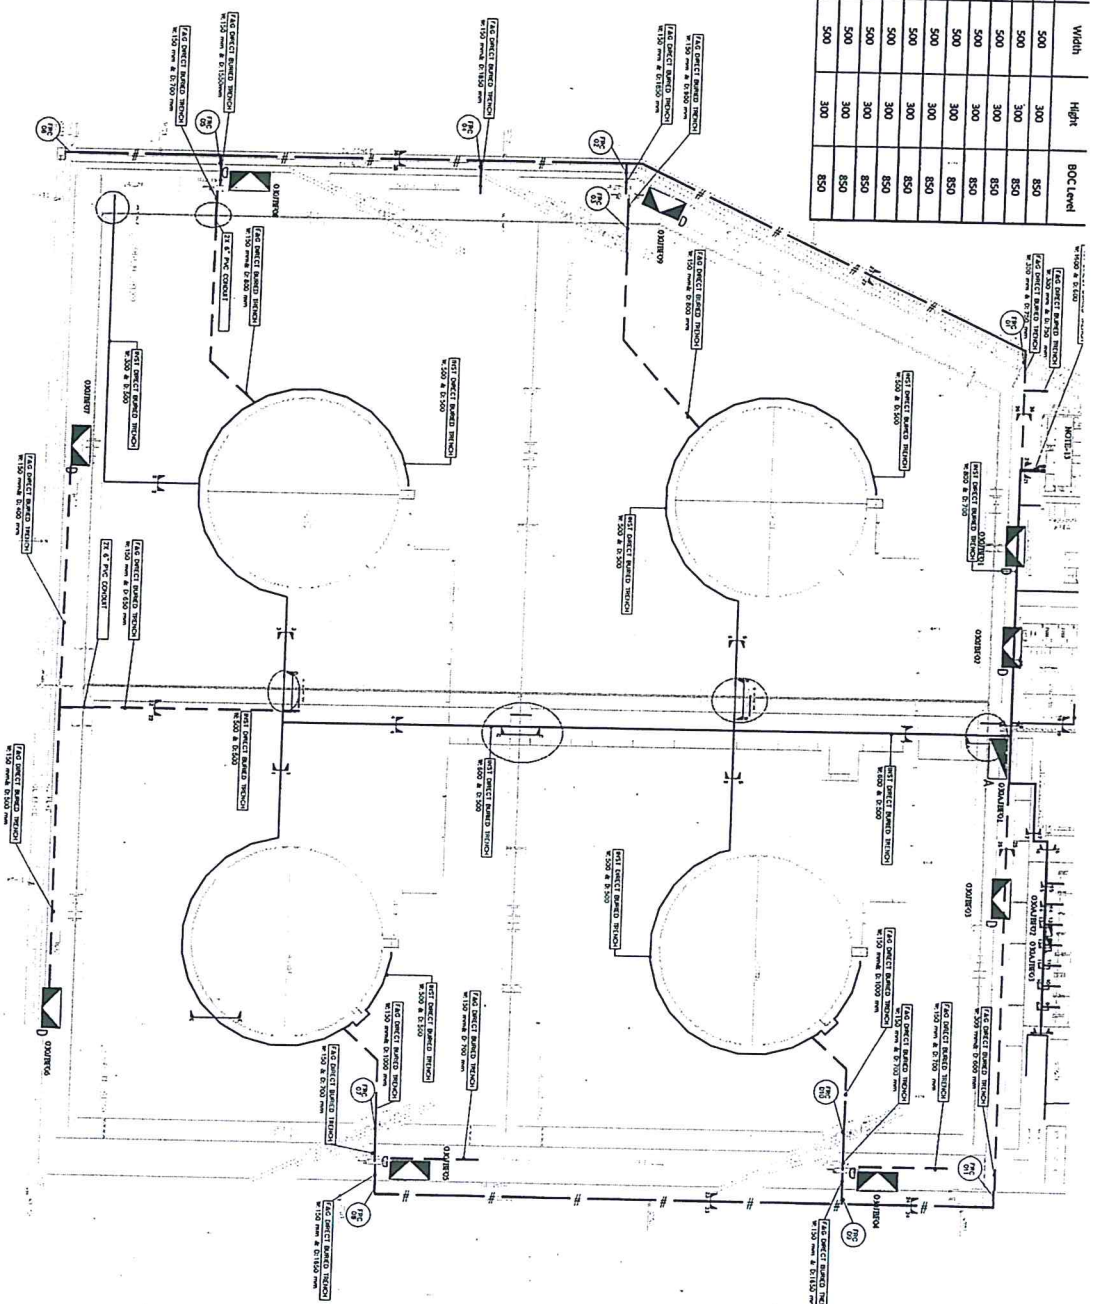

1. ALL DRAFT

2. ALL LATE

3. ALL HIGH

4. DETECTION

5. THE DES

6. THE DES

7. THE DES

8. THE DES

9. THE DES

10. THE DES

11. THE DES

12. THE DES

13. THE DES

14. THE DES

15. THE DES

16. THE DES

17. THE DES

18. THE DES

19. THE DES

20. THE DES

21. THE DES

22. THE DES

23. THE DES

24. THE DES

25. THE DES

26. THE DES

27. THE DES

28. THE DES

29. THE DES

30. THE DES

31. THE DES

32. THE DES

33. THE DES

34. THE DES

35. THE DES

36. THE DES

37. THE DES

38. THE DES

39. THE DES

40. THE DES

41. THE DES

42. THE DES

43. THE DES

44. THE DES

45. THE DES

46. THE DES

47. THE DES

48. THE DES

49. THE DES

50. THE DES

51. THE DES

52. THE DES

53. THE DES

54. THE DES

55. THE DES

56. THE DES

57. THE DES

58. THE DES

59. THE DES

60. THE DES

61. THE DES

62. THE DES

63. THE DES

64. THE DES

65. THE DES

66. THE DES

67. THE DES

68. THE DES

69. THE DES

70. THE DES

71. THE DES

72. THE DES

73. THE DES

74. THE DES

75. THE DES

76. THE DES

77. THE DES

78. THE DES

79. THE DES

80. THE DES

81. THE DES

82. THE DES

83. THE DES

84. THE DES

85. THE DES

86. THE DES

87. THE DES

88. THE DES

89. THE DES

90. THE DES

91. THE DES

92. THE DES

93. THE DES

94. THE DES

95. THE DES

96. THE DES

97. THE DES

98. THE DES

99. THE DES

100. THE DES

10. SPECIAL

11. SPECIAL

12. SPECIAL

13. SPECIAL

14. SPECIAL

15. SPECIAL

16. SPECIAL

17. SPECIAL

18. SPECIAL

19. SPECIAL

20. SPECIAL

21. SPECIAL

22. SPECIAL

23. SPECIAL

24. SPECIAL

25. SPECIAL

26. SPECIAL

27. SPECIAL

28. SPECIAL

29. SPECIAL

30. SPECIAL

31. SPECIAL

32. SPECIAL

33. SPECIAL

34. SPECIAL

35. SPECIAL

36. SPECIAL

37. SPECIAL

38. SPECIAL

39. SPECIAL

40. SPECIAL

41. SPECIAL

42. SPECIAL

43. SPECIAL

44. SPECIAL

45. SPECIAL

46. SPECIAL

47. SPECIAL

48. SPECIAL

49. SPECIAL

50. SPECIAL

51. SPECIAL

52. SPECIAL

53. SPECIAL

54. SPECIAL

55. SPECIAL

56. SPECIAL

57. SPECIAL

58. SPECIAL

59. SPECIAL

60. SPECIAL

61. SPECIAL

62. SPECIAL

63. SPECIAL

64. SPECIAL

65. SPECIAL

66. SPECIAL

67. SPECIAL

68. SPECIAL

69. SPECIAL

70. SPECIAL

71. SPECIAL

72. SPECIAL

73. SPECIAL

74. SPECIAL

75. SPECIAL

76. SPECIAL

77. SPECIAL

78. SPECIAL

79. SPECIAL

80. SPECIAL

81. SPECIAL

82. SPECIAL

83. SPECIAL

84. SPECIAL

85. SPECIAL

86. SPECIAL

87. SPECIAL

88. SPECIAL

89. SPECIAL

90. SPECIAL

91. SPECIAL

92. SPECIAL

93. SPECIAL

94. SPECIAL

95. SPECIAL

96. SPECIAL

97. SPECIAL

98. SPECIAL

99. SPECIAL

100. SPECIAL

1. ALL DRAFT

2. ALL LATE

3. ALL HIGH

4. DETECTION

5. THE DES

6. THE DES

7. THE DES

8. THE DES

9. THE DES

10. THE DES

11. THE DES

12. THE DES

13. THE DES

14. THE DES

15. THE DES

16. THE DES

17. THE DES

18. THE DES

19. THE DES

20. THE DES

21. THE DES

22. THE DES

23. THE DES

24. THE DES

25. THE DES

26. THE DES

27. THE DES

28. THE DES

29. THE DES

30. THE DES

31. THE DES

32. THE DES

33. THE DES

34. THE DES

35. THE DES

36. THE DES

37. THE DES

38. THE DES

39. THE DES

40. THE DES

41. THE DES

42. THE DES

43. THE DES

44. THE DES

45. THE DES

46. THE DES

47. THE DES

48. THE DES

49. THE DES

50. THE DES

51. THE DES

52. THE DES

53. THE DES

54. THE DES

55. THE DES

56. THE DES

57. THE DES

58. THE DES

59. THE DES

60. THE DES

61. THE DES

62. THE DES

63. THE DES

64. THE DES

65. THE DES

66. THE DES

67. THE DES

68. THE DES

69. THE DES

70. THE DES

71. THE DES

72. THE DES

73. THE DES

74. THE DES

75. THE DES

76. THE DES

77. THE DES

78. THE DES

79. THE DES

80. THE DES

81. THE DES

82. THE DES

83. THE DES

84. THE DES

85. THE DES

86. THE DES

87. THE DES

88. THE DES

89. THE DES

90. THE DES

91. THE DES

92. THE DES

93. THE DES

94. THE DES

95. THE DES

96. THE DES

97. THE DES

98. THE DES

99. THE DES

100. THE DES

1:1000











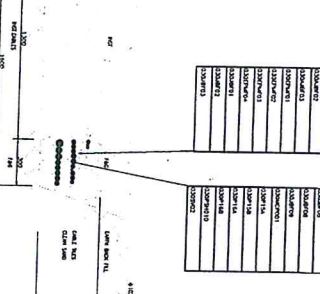

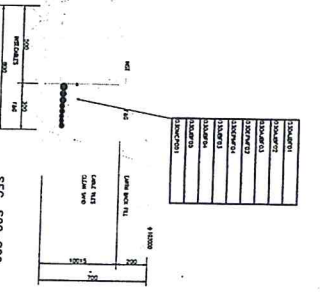
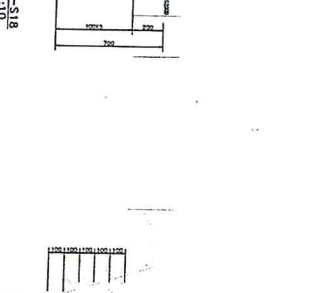
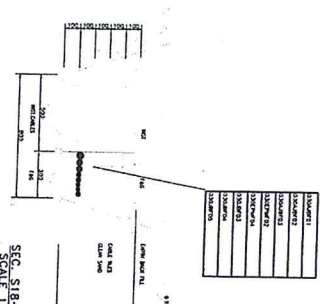
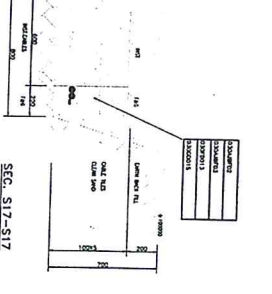
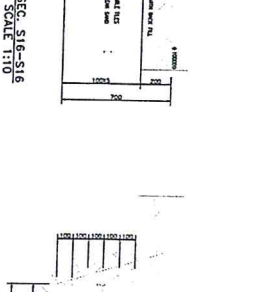
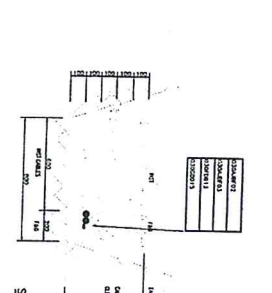
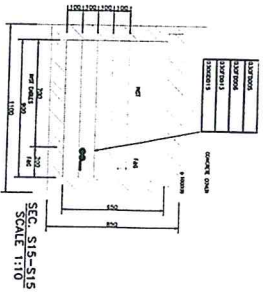
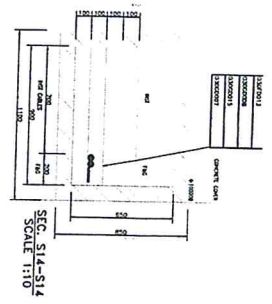
01231-

1:1000

01231-

1:1000

01231-





Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

12.06- Electrical Cables Testing Certificates



ENPPI

EGPC CRUDE OIL TANK FARM



INSPECTION AND TEST REPORT FOR

CABLE INSULATION RESISTANCE TEST

INSPECTION REPORT NUMBER

REF: 117/84

INSTRUMENT TYPE:

INSPECTION DATE & TIME

DOCUMENT NO.

ITR-EL-0006A

DISCIPLINE

ELECTRICAL

SHEET NO.

SYSTEM NO.:

TEST VOLTAGE:

AREA / PACKAGE:

SERIAL:

220 V

TEST VOLTAGE:

11V

N	Item/Tag NO.	CABLE SIZE	Continuity Test	PHASE TO PHASE "M.Ohm"	PHASE TO NEUTRAL "M.Ohm"	PHASES & NEUTRAL TO ARMOR "M.Ohm"	RESULT
1	030-FD-004	1*3*2.5	✓	BR-BK	BR-GR	BR-GR	Pass
2	030-GD-004	1*3*2.5	✓	BR-BK	BR-GR	BR-GR	Pass
3	030-LHD-007	1*2*1.5	✓	BR-BK	BR-GR	BR-GR	Pass
4	030-LHD-008	1*2*1.5	✓	BR-BK	BR-GR	BR-GR	Pass
5							
6							
7							
8							
9							
10							
11							
12							
13							
14							
15							
16							
17							
18							
19							

Remarks :-

Reference :-

PETROJET

ENPPI

PMC

NAME :

SIGNATURE

DATE

Islam Sherif



Enppi

ENPPI

EGPC CRUDE OIL TANK FARM



INSPECTION AND TEST REPORT FOR

CABLE INSULATION RESISTANCE TEST

SYSTEM NO.:

INSPECTION REPORT NUMBER
PTJ-INST-RFI-80

INSPECTION DATE & TIME

DOCUMENT NO.
ITR-EL-0006B

DISCIPLINE
INST

SHEET NO

INSTRUMENT TYPE:

FLUKE 1507 INSULATION TESTER

SERIAL:
46240215WS

SERVICE VOLTAGE:
24

TEST VOLTAGE:
250

AREA / PACKAGE:

NO	Item/Tag NO.	CABLE SIZE	Continuity Test	pair conductors	conductors to armor	Shield to Shield	All Conductors-GND	Overall Shield -GND	Armor-GND	RESULT
1	030-STR-002	1X2X2.5	✓	25-0				2270.4Ω		✓
2	030-STB-002	1X2X2.5	✓							✓
3	030-HR-002	1X2X2.5	✓							✓
4	030-PSH-001 A	1X2X2.5	✓							✓
5	030-PSH-001 B	1X2X2.5	✓							✓
6	030-PSH-001 C	1X2X2.5	✓							✓
7	030-PSH-001 D	1X2X2.5	✓							✓
8	030-PSH-003 A	1X2X2.5	✓							✓
9	030-PSH-003 B	1X2X2.5	✓							✓
10	030-PSH-003 C	1X2X2.5	✓							✓
11	030-PSH-003 D	1X2X2.5	✓							✓
12	030-PSH-007 A	1X2X2.5	✓							✓
13	030-PSH-007 B	1X2X2.5	✓							✓
14	030-PSH-007 C	1X2X2.5	✓							✓
15	030-PSH-007 D	1X2X2.5	✓	25-0				2270.4Ω		✓
16										
17										

Remarks :-

Reference

NAME:	PETROJET	ENPPI	PMC
SIGNATURE		Islam Sherif	
DATE			



ENPPI

EGPC CRUDE OIL TANK FARM



INSPECTION AND TEST REPORT FOR

CABLE INSULATION RESISTANCE TEST

INSPECTION REPORT NUMBER

RFI-177

INSTRUMENT TYPE:

INSPECTION DATE & TIME

SERIAL:

SERVICE VOLTAGE:

220 v

DOCUMENT NO.

ITR-EL-0006A

DISCIPLINE

ELECTRICAL

SHEET NO

AREA / PACKAGE:

SYSTEM NO.:

N O	Item/Tag NO.	CABLE SIZE	Continuity Test	PHASE TO PHASE "M.Ohm"			PHASE TO NEUTRAL "M.Ohm"			PHASES & NEUTRAL TO ARMOR "M.Ohm"			RESULT	
				BR-BK	BR-GR	BK-GR	BR-B	BK-B	GR-B	BR-ARM	BK-ARM	GR-ARM	B-ARM	Pass FAIL
1	030-PSH-4002	1*2*1.5	✓	Phase to phase (o.v.)										✓
2	030-PSH-4004	1*2*1.5	✓											✓
3	030-PSH-4006	1*2*1.5	✓											✓
4	030-PSH-4008	1*2*1.5	✓											✓
5	030-MCP-001	1*2*1.5	✓											✓
6	030-JRF-002	8*2*1.5	✓											✓
7														
8														
9														
10														
11														
12														
13														
14														
15														
16														
17														
18														
19														

Remarks :-

Reference :-

NAME :	PETROJET	ENPPI	PMC
SIGNATURE		Islam Sherif	
DATE			

ITR-EL-0006A



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

12.07- Electrical Cables Termination Certificates

**Enppi****EGPC CRUDE OIL TANK FARM**Owner : **Egyptian General Petroleum Corporation (EGPC)**Project No: 01251-100-030
:01251-100-031Contractor **CONSORTIUM (ENPPI / PETROJET)**Document No: ITR-QC-0001
Revision No. : 00**REQUEST FOR INSPECTION**ACTIVITY : **INSTRUMENT INSTALLATION**NOTIFICATION NO. : **PTJ-INS-RFI- 59** DISCIPLINE : **E&I**DATE : **5/20/2021**

NO.	DESCRIPTION	LOCATION	DATE / TIME	INSPECTION			REMARKS
				PETROJET	ENPPI	PMC	
	INSTRUMENT INSTALLATION	MODULE 1	20-May-21				
1	030-PSH-002						
2	030-PSH-004						
3	030-PSH-006						
4	030-PSH-008						
5	030-PSH-001A						
6	030-PSH-001B						
7	030-PSH-001C						
8	030-PSH-001D						
9	030-PSH-007A						
10	030-PSH-007B						
11	030-PSH-007C						
12	030-PSH-007D						
13							
14							
15							
16							
17							
18							

NOTE:

Inspection result : A - Approved B - Reject C - Approved with Comment

tag no to be install. (Dar) Sobh

	PETROJET	ENPPI	PMC
NAME :			
SIGNATURE	<i>Sobh</i>	<i>Islam Sherrif</i>	<i>M. Omar</i>
DATE			

ITR-QC-0001



EGPC CRUDE OIL TANK FARM
AGROOD AREA (MODULE 1 & 2)



INSPECTION AND TEST REPORT FOR

INSTRUMENT INSTALLATION

INSPECTION REPORT NUMBER RFI-59	INSPECTION DATE & TIME	ITR NUMBER ITR-IC-0001	DISPLINE INSTRUMENT	SHEET NO
------------------------------------	------------------------	---------------------------	------------------------	----------

JOB DESCRIPTION		AREA DESCRIPTION	
ENGINEERING DOCUMENT NUMBER		SYSTEM NUMBER(IF APPLICABLE)	SUBCONTRACTOR/SUPPLIER
ITEM / TAG NO.		TYPE	

NO.	INSPECTION	RESULT		
		ACCEPT	REJECT	N/A.
1	No physical damage are found	✓		
2	Type / size / location as per drawings and vendor data sheet	✓		
3	Identification / name plate attached correctly		✓	
4	Stanchion type / mounting as per drawings	✓		
5	Welding (if required) and touch up	✓		
6	Anchor bolting / Bolt tightening	✓		
7	Grouting (if required)			✓
8	Orientation / direction as per drawings	✓		
9	Accessibility	✓		
10	Assembling compartments properly installed	✓		
11	Earthing and bonding properly installed		✓	
12	Cleanliness	✓		

REMARKS:

REFERENCE DOCUMENTS:

SUBCONTRACTOR	PETROJET	ENPPI	PMC
NAME	NAME	NAME	NAME
SIGNATURE	SIGNATURE <i>Sobh</i>	SIGNATURE <i>Wahid Sherif</i>	SIGNATURE <i>M. Omar</i>
DATE	DATE	DATE	DATE

ITR-CI-0001.

**Enppi**

EGPC CRUDE OIL TANK FARM



Owner : Egyptian General Petroleum Corporation (EGPC)

Project No: 01251-100-030
:01251-100-031

Contractor CONSORTIUM (ENPPI / PETROJET)

Document No: ITR-QC-0001
Revision No. : 00**REQUEST FOR INSPECTION**

ACTIVITY : CABLE TERMINATION AND SPLICING AND INSTALLATION

NOTIFICATION NO. : PTJ-INS-RFI- 79 DISCIPLINE : E&I

DATE : 6/9/2021

NO.	DESCRIPTION	LOCATION	DATE / TIME	INSPECTION			REMARKS
				PETROJET	ENPPI	PMC	
	CABLE TERMINATION AND SPLICING AND INSTALLATION	MODULE 1	9-Jun-21				
1	030-PSH-002	}					1. Cables to layed in the trench and backfilled with soft sand (Done) Sobh 2. S.S. tray missing in both sides (Done) Sobh 3. cables to be systemized in cable tray (Done) Sobh 4. Cable tray cover missing (none) (Sobh)
2	030-PSH-004						
3	030-PSH-006						
4	030-PSH-008						
5	030-MCP-001						
6	030-JBF-002						
7							
8							
9							
10							
11							
12							
13							
14							
15							
16							
17							
18							
19							

NOTE:

Inspection result : A - Approved B - Reject C - Approved with Comment

	PETROJET	ENPPI	PMC
NAME :			
SIGNATURE			
DATE			

ITR-QC-0001



EGPC CRUDE OIL TANK FARM



INSPECTION AND TEST REPORT FOR

CABLE TERMINATION AND SPLICING

SYSTEM NO.:

INSPECTION REPORT NUMBER

INSPECTION DATE & TIME

ITR NUMBER

ITR-EL-0009

DISCIPLINE

ELEC

SHEET NO

1 OF 1

Item/Tag NO.

Type :-

Core:

Size:

NO.	Description of check	RESULT		
		ACCEPT	REJECT	N/A.
1	Check cable glands are correct type and size as per cable schedule.	✓		
2	Check there are no damages to cores, termination chamber layout is satisfactory, core identification is correct, crimped and pins satisfactory.	✓		
3	Check cable tag is done correctly.		✓	
4	Test and confirm conductor, phase continuity.	✓		
5	Check insulation resistance test (megger) is completed *I	✓		
6	Check Hi-pot test is completed, only for MV/HV cables *II			✓
7	Connect all cores at both ends and confirm all connections are correct as per termination diagram.	✓		
8	Confirm spare cores, screens are earthed and conform to design drawings/specifications	✓		
9	Check enclosure cover is installed, no damages and no bolts are missing	✓		
10	Calibration test certificate of testing equipment to be checked.			✓

Remarks :

	PETROJET	ENPPI	PMC
NAME :			
SIGNATURE			
DATE			

ITR-EL-0009

**Enppi****EGPC CRUDE OIL TANK FARM**Owner: **Egyptian General Petroleum Corporation (EGPC)**Project No: 01251-100-030
:01251-100-031Contractor **CONSORTIUM (ENPPI / PETROJET)**Document No: ITR-QC-0001
Revision No. : 00**REQUEST FOR INSPECTION**ACTIVITY : **F&G DEVICE TERMINATION**NOTIFICATION NO. : **PTJ-INST-RFI-80** DISCIPLINE : **F&G**DATE : **6/10/2021**

NO.	DESCRIPTION	LOCATION	DATE / TIME	INSPECTION			REMARKS
				PETROJET	ENPPI	PMC	
	F&G device TERMINATION	Field	10-Jun-21				
1	030-STR-002						
2	030-STB-002						
3	030-HR-002						
4	030-PSH-001 A						
5	030-PSH-001 B						
6	030-PSH-001 C						
7	030-PSH-001 D						
8	030-PSH-003 A						
9	030-PSH-003 B						
10	030-PSH-003 C						
11	030-PSH-003 D						
12	030-PSH-007 A						
13	030-PSH-007 B						
14	030-PSH-007 C						
15	030-PSH-007 D						
16							
17							
18							
19							
20							
21							
22							
23							
24							
25							
26							
27							

NOTE:

Inspection result : A - Approved B - Reject C - Approved with Comment

all tags must be installed. (Done) SOB

	PETROJET	ENPPI	PMC
NAME :			
SIGNATURE	<i>[Signature]</i>	<i>[Signature]</i>	<i>[Signature]</i>
DATE			



EGPC CRUDE OIL TANK FARM



INSPECTION AND TEST REPORT FOR

CABLE TERMINATION AND SPLICING

SYSTEM NO.:

INSPECTION REPORT NUMBER

INSPECTION DATE & TIME

ITR NUMBER

DISCIPLINE

SHEET NO

PTJ-INST-RFI-

ITR-EL-0009

INST

1 OF 1

Item/Tag NO.

Type :-

Core:

Size:

NO.	Description of check	RESULT		
		ACCEPT	REJECT	N/A.
1	Check cable glands are correct type and size as per cable schedule.	✓		
2	Check there are no damages to cores, termination chamber layout is satisfactory, core identification is correct, crimped and pins satisfactory.	✓		
3	Check cable tag is done correctly.			✓
4	Test and confirm conductor, phase continuity.	✓		
5	Check insulation resistance test (megger) is completed *I	✓		
6	Check Hi-pot test is completed, only for MV/HV cables *II	✓		✓
7	Connect all cores at both ends and confirm all connections are correct as per termination diagram.	✓		
8	Confirm spare cores, screens are earthed and conform to design drawings/specifications			✓
9	Check enclosure cover is installed, no damages and no bolts are missing			✓
10	Calibration test certificate of testing equipment to be checked.			✓

Remarks :

*I : ITR-EL-006A/B

*II : ITR-EL-008

	PETROJET	ENPPI	PMC
NAME :			
SIGNATURE			
DATE			

ITR-EL-0009

**Enppi****EGPC CRUDE OIL TANK FARM**Owner : **Egyptian General Petroleum Corporation (EGPC)**Project No: 01251-100-030
:01251-100-031Contractor **CONSORTIUM (ENPPI / PETROJET)**Document No: ITR-QC-0001
Revision No. : 00**REQUEST FOR INSPECTION**ACTIVITY : **INSTRUMENT INSTALLATION & TERMINATION**NOTIFICATION NO. : **PTJ-INS-RFI- 84** DISCIPLINE : **E&I**DATE : **6/16/2021**

NO.	DESCRIPTION	LOCATION	DATE / TIME	INSPECTION			REMARKS
				PETROJET	ENPPI	PMC	
	INSTRUMENT INSTALLATION & TERMINATION	MODULE 1	16-Jun-21				
1	030-FD-004						
2	030-GD-004						
3	030-LHD-007						
4	030-LHD-008						
5							
6							
7							
8							
9							
10							
11							
12							
13							
14							
15							
16							
17							
18							
19							

NOTE:

Inspection result : A - Approved B - Reject C - Approved with Comment

All Tags must be installed.

	PETROJET	ENPPI	PMC
NAME :			
SIGNATURE	<i>Sah</i>	<i>Islam Sherif</i>	<i>RH</i>
DATE			

ITR-QC-0001



EGPC CRUDE OIL TANK FARM



INSPECTION AND TEST REPORT FOR

CABLE TERMINATION AND SPLICING

SYSTEM NO.:

INSPECTION REPORT NUMBER

RSI-84

INSPECTION DATE & TIME

ITR NUMBER

ITR-EL-0009

DISCIPLINE

ELEC

SHEET NO

1 OF 1

Item/Tag NO.

Type :-

Core:

Size:

NO.	Description of check	RESULT		
		ACCEPT	REJECT	N/A.
1	Check cable glands are correct type and size as per cable schedule.	✓		
2	Check there are no damages to cores, termination chamber layout is satisfactory, core identification is correct, crimped and pins satisfactory.	✓		
3	Check cable tag is done correctly.		✓	
4	Test and confirm conductor, phase continuity.	✓		
5	Check insulation resistance test (megger) is completed **	✓		
6	Check Hi-pot test is completed, only for MV/HV cables ***			✓
7	Connect all cores at both ends and confirm all connections are correct as per termination diagram.	✓		
8	Confirm spare cores, screens are earthed and conform to design drawings/specifications	✓		
9	Check enclosure cover is installed, no damages and no bolts are missing	✓		
10	Calibration test certificate of testing equipment to be checked.			✓

Remarks :

	PETROJET	ENPPI	PMC
NAME :			
SIGNATURE			
DATE			

ITR-EL-0009



EGPC CRUDE OIL TANK FARM
AGROOD AREA (MODULE 1 & 2)



INSPECTION AND TEST REPORT FOR

INSTRUMENT INSTALLATION

INSPECTION REPORT NUMBER Rft-84	INSPECTION DATE & TIME	ITR NUMBER ITR-IC-0001	DISCIPLINE INSTRUMENT	SHEET NO
---	------------------------	---------------------------	--------------------------	----------

JOB DESCRIPTION		AREA DESCRIPTION		
ENGINEERING DOCUMENT NUMBER		SYSTEM NUMBER (IF APPLICABLE)	SUBCONTRACTOR/SUPPLIER	
ITEM / TAG NO.		TYPE		

NO.	INSPECTION	RESULT		
		ACCEPT	REJECT	N/A
1	No physical damage are found	✓		
2	Type / size / location as per drawings and vendor data sheet	✓		
3	Identification / name plate attached correctly		✓	
4	Stanchion type / mounting as per drawings	✓		
5	Welding (if required) and touch up			✓
6	Anchor bolting / Bolt tightening	✓		
7	Grouting (if required)			✓
8	Orientation / direction as per drawings	✓		
9	Accessibility	✓		
10	Assembling compartments properly installed	✓		
11	Earthing and bonding properly installed	✓		
12	Cleanliness	✓		

REMARKS:

REFERENCE DOCUMENTS:

SUBCONTRACTOR	PETROJET	ENPPI	PMC
NAME	NAME	NAME	NAME
SIGNATURE	SIGNATURE <i>Solt</i>	SIGNATURE <i>Islam Sherif</i>	SIGNATURE <i>[Signature]</i>
DATE	DATE	DATE	DATE

ITR-CI-0001



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

12.08- FAT Reports & Certificates



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)





System ID	030-LP-008
System Description	Tank-4 Fire Protection System

12.09- SAT Reports & Certificates

System ID	030-LP-008
System Description	Tank-4 Fire Protection System

12.10- Electrical Pre-Commissioning Check Lists

PRE-COMMISSIONING CHECK LIST DETECTOR LP-13 A			
PROJECT TITLE : EGPC Crude Oil Tank Farms Project, Agrood Area 30 (Module-01)			
PROJECT NUMBER : 1251-100		DISCIPLINE : Loss Prevention	
SYSTEM NAME : Tank-4 Fire Protection System		SYSTEM ID : 030-LP-008	
SUB-SYSTEM NAME : Tank-4 Fire Protection System		SUB-SYSTEM ID : 030-LP-008	
ITEM TAG No. : 030-GD-004		AREA : 30	
REF. DWGs/DOCs : 030-GD-004			
No.	DESCRIPTION	RESULT OK/NA/PL	PL ITEM No.
1	FIRE AND GAS DETECTOR:		
1.1	Detector placed in the correct location as per the distribution drawings.	✓	
1.2	Detector placed in the correct elevation as per the distribution drawings.	✓	
1.3	Detector mounted in the correct orientation as per common engineering practice.	✓	
1.4	Outlet tags are according to the drawing & correctly placed.	✓	
1.5	Detector is in good condition and has no physical/mechanical damage.	✓	
1.6	Detector is properly fixed.	✓	
1.7	Detector type and model number are as mentioned in the drawings/purchase order.	✓	
1.8	Check accessibility for maintenance.	✓	
1.9	Check that there are no missing parts.	✓	
1.10	Check/perform Pre-comm. check lists for all cables connected/wired to the outlet.	✓	
REMARKS AND OBSERVATIONS :			
OK: NO OBJECTION, NA: NOT APPLICABLE, PL: PUNCH LIST.			
COMPANY	PETROJET	ENPPI	PPC
NAME		Islam Sherif	Mohamed Omar
SIGNATURE			M. Omar
DATE			

PRE-COMMISSIONING CHECK LIST			
DETECTOR			
LP-13 A			
PROJECT TITLE : EGPC Crude Oil Tank Farms Project, Agrood Area 30 (Module-01)			
PROJECT NUMBER : 1251-100		DISCIPLINE : Loss Prevention	
SYSTEM NAME : Tank-4 Fire Protection System		SYSTEM ID : 030-LP-008	
SUB-SYSTEM NAME : Tank-4 Fire Protection System		SUB-SYSTEM ID : 030-LP-008	
ITEM TAG No. : 030-FD-004		AREA : 30	
REF. DWGs/DOCs : 030-FD-004			
No.	DESCRIPTION	RESULT	PL
		OK/NA/PL	ITEM No.
1	FIRE AND GAS DETECTOR:		
1.1	Detector placed in the correct location as per the distribution drawings.	✓	
1.2	Detector placed in the correct elevation as per the distribution drawings.	✓	
1.3	Detector mounted in the correct orientation as per common engineering practice.	✓	
1.4	Outlet tags are according to the drawing & correctly placed.	✓	
1.5	Detector is in good condition and has no physical/mechanical damage.	✓	
1.6	Detector is properly fixed.	✓	
1.7	Detector type and model number are as mentioned in the drawings/purchase order.	✓	
1.8	Check accessibility for maintenance.	✓	
1.9	Check that there are no missing parts.	✓	
1.10	Check/perform Pre-comm. check lists for all cables connected/wired to the outlet.	✓	
REMARKS AND OBSERVATIONS :			
OK: NO OBJECTION, NA: NOT APPLICABLE, PL: PUNCH LIST.			
COMPANY	PETROJET	ENPPI	PPC
NAME			mo hamed omar
SIGNATURE			m. o mar
DATE			



**PRE-COMMISSIONING CHECK LIST
DETECTOR
LP-13 A**



PROJECT TITLE	: EGPC Crude Oil Tank Farms Project, Agrood Area 30 (Module-01)		
PROJECT NUMBER	: 1251-100	DISCIPLINE	: Loss Prevention
SYSTEM NAME	: Tank-4 Fire Protection System	SYSTEM ID	: 030-LP-008
SUB-SYSTEM NAME	: Tank-4 Fire Protection System	SUB-SYSTEM ID	: 030-LP-008
ITEM TAG No.	: 030-LHD-007	AREA	: 30
REF. DWGs/DOCs	: 030-LHD-007		

No.	DESCRIPTION	RESULT	PL
		OK/NA/PL	ITEM No.
1	FIRE AND GAS DETECTOR:		
1.1	Detector placed in the correct location as per the distribution drawings.	✓	
1.2	Detector placed in the correct elevation as per the distribution drawings.	✓	
1.3	Detector mounted in the correct orientation as per common engineering practice.	✓	
1.4	Outlet tags are according to the drawing & correctly placed.	✓	
1.5	Detector is in good condition and has no physical/mechanical damage.	✓	
1.6	Detector is properly fixed.	✓	
1.7	Detector type and model number are as mentioned in the drawings/purchase order.	✓	
1.8	Check accessibility for maintenance.	✓	
1.9	Check that there are no missing parts.	✓	
1.10	Check/perform Pre-comm. check lists for all cables connected/wired to the outlet.	✓	

REMARKS AND OBSERVATIONS :

OK: NO OBJECTION, NA: NOT APPLICABLE, PL: PUNCH LIST.

COMPANY	PETROJET	ENPPI	PPC
NAME		Islam Sherif	Mahamed Omar
SIGNATURE			M. Omar
DATE			

PRE-COMMISSIONING CHECK LIST			
DETECTOR			
LP-13 A			
PROJECT TITLE : EGPC Crude Oil Tank Farms Project, Agrood Area 30 (Module-01)			
PROJECT NUMBER : 1251-100		DISCIPLINE : Loss Prevention	
SYSTEM NAME : Tank-4 Fire Protection System		SYSTEM ID : 030-LP-008	
SUB-SYSTEM NAME : Tank-4 Fire Protection System		SUB-SYSTEM ID : 030-LP-008	
ITEM TAG No. : 030-LHD-008		AREA : 30	
REF. DWGs/DOCs : 030-LHD-008			
No.	DESCRIPTION	RESULT	PL
		OK/NA/PL	ITEM No.
1	FIRE AND GAS DETECTOR:		
1.1	Detector placed in the correct location as per the distribution drawings.	✓	
1.2	Detector placed in the correct elevation as per the distribution drawings.	✓	
1.3	Detector mounted in the correct orientation as per common engineering practice.	✓	
1.4	Outlet tags are according to the drawing & correctly placed.	✓	
1.5	Detector is in good condition and has no physical/mechanical damage.	✓	
1.6	Detector is properly fixed.	✓	
1.7	Detector type and model number are as mentioned in the drawings/purchase order.	✓	
1.8	Check accessibility for maintenance.	✓	
1.9	Check that there are no missing parts.	✓	
1.10	Check/perform Pre-comm. check lists for all cables connected/wired to the outlet.	✓	
REMARKS AND OBSERVATIONS :			
OK: NO OBJECTION, NA: NOT APPLICABLE, PL: PUNCH LIST.			
COMPANY	PETROJET	ENPPI	PPC
NAME			Mohamed Omar
SIGNATURE			M. Omar
DATE			



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

12.11- Electrical Supplier Check Lists & Reports



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

13- Electrical Commissioning



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

13.01- Electrical -Commissioning Check Lists

System ID	030-LP-008
System Description	Tank-4 Fire Protection System

13.02- Electrical Supplier Check Lists & Reports



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

14- Red Marked-up Drawings



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

14.01- P&ID



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

14.02- Instrumentation Drawings



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-LP-008
System Description	Tank-4 Fire Protection System

14.03- Electrical Drawings
